
Activity ID	Activity Name	Original Duration	Start	Finish
KBR Keane's Bar & Restaurant, NY		122	20-Apr-26	26-Oct-26
KBR.1 GENERAL CONDITIONS		122	20-Apr-26	26-Oct-26
A1000	Project Kickoff & Subcontractor Mobilization	0	20-Apr-26	
A1010	Site Protection, Hoarding & Temporary Signage	2	20-Apr-26	22-Apr-26
A1020	Temporary Utilities (Power, Water, Lighting)	2	20-Apr-26	21-Apr-26
A1030	Dumpster Setup & Waste Management Plan	1	20-Apr-26	20-Apr-26
A1040	Project Management & Supervision	122	20-Apr-26	26-Oct-26
A1050	Insurance, Permits & NYC/Westchester Filing	8	20-Apr-26	30-Apr-26
A1060	Site Safety Plan & OSHA Compliance Setup	2	20-Apr-26	21-Apr-26
KBR.2 DEMOLITION & STRUCTURAL		20	22-Apr-26	22-May-26
A1070	Selective Interior Demolition Walls & Partitions	6	22-Apr-26	30-Apr-26
A1080	Demolition – Existing Bar & Millwork Removal	3	30-Apr-26	06-May-26
A1090	Demolition – Ceiling & Soffit Removal	2	30-Apr-26	05-May-26
A1100	Demolition – Existing Flooring Removal (All Area	3	30-Apr-26	06-May-26
A1110	Concrete Cutting – Kitchen Trench for Drains	4	06-May-26	12-May-26
A1120	Concrete Trenching – Bar Area Plumbing Rough	3	12-May-26	18-May-26
A1130	Structural Reinforcement – Beam/Column Asse	4	06-May-26	12-May-26
A1140	Structural Reinforcement – New Opening Head	5	12-May-26	20-May-26
A1150	Debris Hauling & Final Demolition Cleanup	2	20-May-26	22-May-26
KBR.3 PLUMBING WORKS		18	12-May-26	10-Jun-26
A1160	Underground Plumbing – Kitchen Drain Lines	5	12-May-26	20-May-26
A1170	Underground Plumbing – Bar Drain Lines & Flo	4	18-May-26	22-May-26
A1180	Underground Plumbing – Restroom Drain Lines	4	12-May-26	19-May-26
A1190	Concrete Patching After Trenching (All Areas)	3	22-May-26	28-May-26
A1200	Rough Plumbing – Supply Lines, Kitchen & Bar	5	01-Jun-26	08-Jun-26
A1210	Rough Plumbing – Restroom Supply & Vent St	4	01-Jun-26	05-Jun-26
A1211	Grease Trap Installation	2	21-May-26	25-May-26
A1220	Rough Plumbing Inspection & Sign-Off	2	08-Jun-26	10-Jun-26
KBR.4 FRAMING & CARPENTRY		16	20-May-26	12-Jun-26
A1230	Metal Stud Framing – Restrooms & Back-of-Ho	5	29-May-26	05-Jun-26
A1240	Metal Stud Framing – Bar Area Partitions	4	25-May-26	01-Jun-26
A1250	Metal Stud Framing – Dining Room Partitions	4	25-May-26	01-Jun-26
A1260	Metal Stud Framing – Mezzanine Area Walls	5	20-May-26	27-May-26
A1270	Wood Framing – Bar Base Structure & Subfram	4	01-Jun-26	05-Jun-26
A1280	Ceiling Framing – Dining Room Coffers & Bulkh	6	01-Jun-26	09-Jun-26
A1290	Ceiling Framing – Bar Area Soffits & Bulkheads	4	03-Jun-26	09-Jun-26
A1300	Ceiling Framing – Kitchen & BOH Areas	3	09-Jun-26	12-Jun-26
A1310	Blocking & Backing – Millwork, TV, Handrails	3	05-Jun-26	11-Jun-26
A1320	Mezzanine Structural Wood/Steel Framing	6	20-May-26	29-May-26
KBR.5 MECHANICAL, ELECTRICAL & PLUMBIN		26	27-May-26	07-Jul-26
A1330	Rough Electrical – Panel Upgrade & Distributior	6	29-May-26	08-Jun-26
A1340	Rough Electrical – Kitchen Circuits & Conduit	5	05-Jun-26	12-Jun-26
A1350	Rough Electrical – Bar Circuits & Low Voltage	4	01-Jun-26	05-Jun-26
A1360	Rough Electrical – Dining & Mezzanine Circuits	5	01-Jun-26	08-Jun-26
A1370	Rough Electrical – Exterior Signage & Lighting	3	03-Jun-26	08-Jun-26
A1380	HVAC Ductwork – Kitchen Exhaust & Supply	6	15-Jun-26	24-Jun-26
A1390	HVAC Ductwork – Dining Room & Bar Distributic	6	09-Jun-26	18-Jun-26
A1400	HVAC Ductwork – Mezzanine & Restrooms	4	27-May-26	02-Jun-26
A1410	Kitchen Hood & Exhaust Fan Rough-In	4	24-Jun-26	30-Jun-26
A1420	Fire Sprinkler Rough-In – All Areas	6	05-Jun-26	16-Jun-26
A1430	Fire Alarm Rough-In & Smoke Detection	4	18-Jun-26	24-Jun-26
A1440	Security, POS & Data Low Voltage Rough-In	4	09-Jun-26	15-Jun-26
A1450	MEP Rough-In Inspection & Sign-Off (Westches	2	03-Jul-26	07-Jul-26
KBR.6 DRYWALL & TAPING		26	07-Jul-26	17-Aug-26
A1460	Insulation – Batt & Acoustic (Walls & Ceilings)	4	07-Jul-26	14-Jul-26
A2060	Drywall Hang – BOH, Kitchen (MR Board)	4	14-Jul-26	20-Jul-26
A1480	Drywall Hang – Restrooms (MR Board)	3	14-Jul-26	17-Jul-26
A1490	Drywall Hang – Bar Area	4	14-Jul-26	20-Jul-26
A1500	Drywall Hang – Dining Room & Mezzanine	6	14-Jul-26	22-Jul-26
A1510	Fire-Rated Assembly Drywall – Kitchen & Stairw	3	20-Jul-26	24-Jul-26
A1520	Tape & First Coat – All Areas	4	22-Jul-26	28-Jul-26
A1530	Second Coat & Sand	4	29-Jul-26	05-Aug-26
A1540	Level 5 Skim Coat – Dining Room & Bar (Visible	5	06-Aug-26	13-Aug-26
A1550	Drywall Final Inspection & Punch	2	13-Aug-26	17-Aug-26
KBR.7 FLOORING PREPARATION		6	17-Aug-26	25-Aug-26
A1560	Self-Leveling Underlayment – Kitchen & BOH	3	17-Aug-26	20-Aug-26
A1570	Self-Leveling Underlayment – Restrooms	2	17-Aug-26	19-Aug-26
A1580	Self-Leveling Underlayment – Bar Area	2	17-Aug-26	19-Aug-26
A1590	Self-Leveling Underlayment – Dining Room	3	17-Aug-26	20-Aug-26
A1600	Curing & Preparation (All Areas)	2	20-Aug-26	25-Aug-26
KBR.8 CEILINGS		22	24-Jul-26	27-Aug-26
A1610	ACT Grid Ceiling – Kitchen & BOH	4	17-Aug-26	21-Aug-26
A1620	Washable Ceiling System – Kitchen (FRP or Sir	3	21-Aug-26	27-Aug-26
A1630	ACT Grid Ceiling – Storage & Utility Rooms	2	17-Aug-26	19-Aug-26
A1640	Decorative Ceiling System – Dining Room	6	13-Aug-26	24-Aug-26

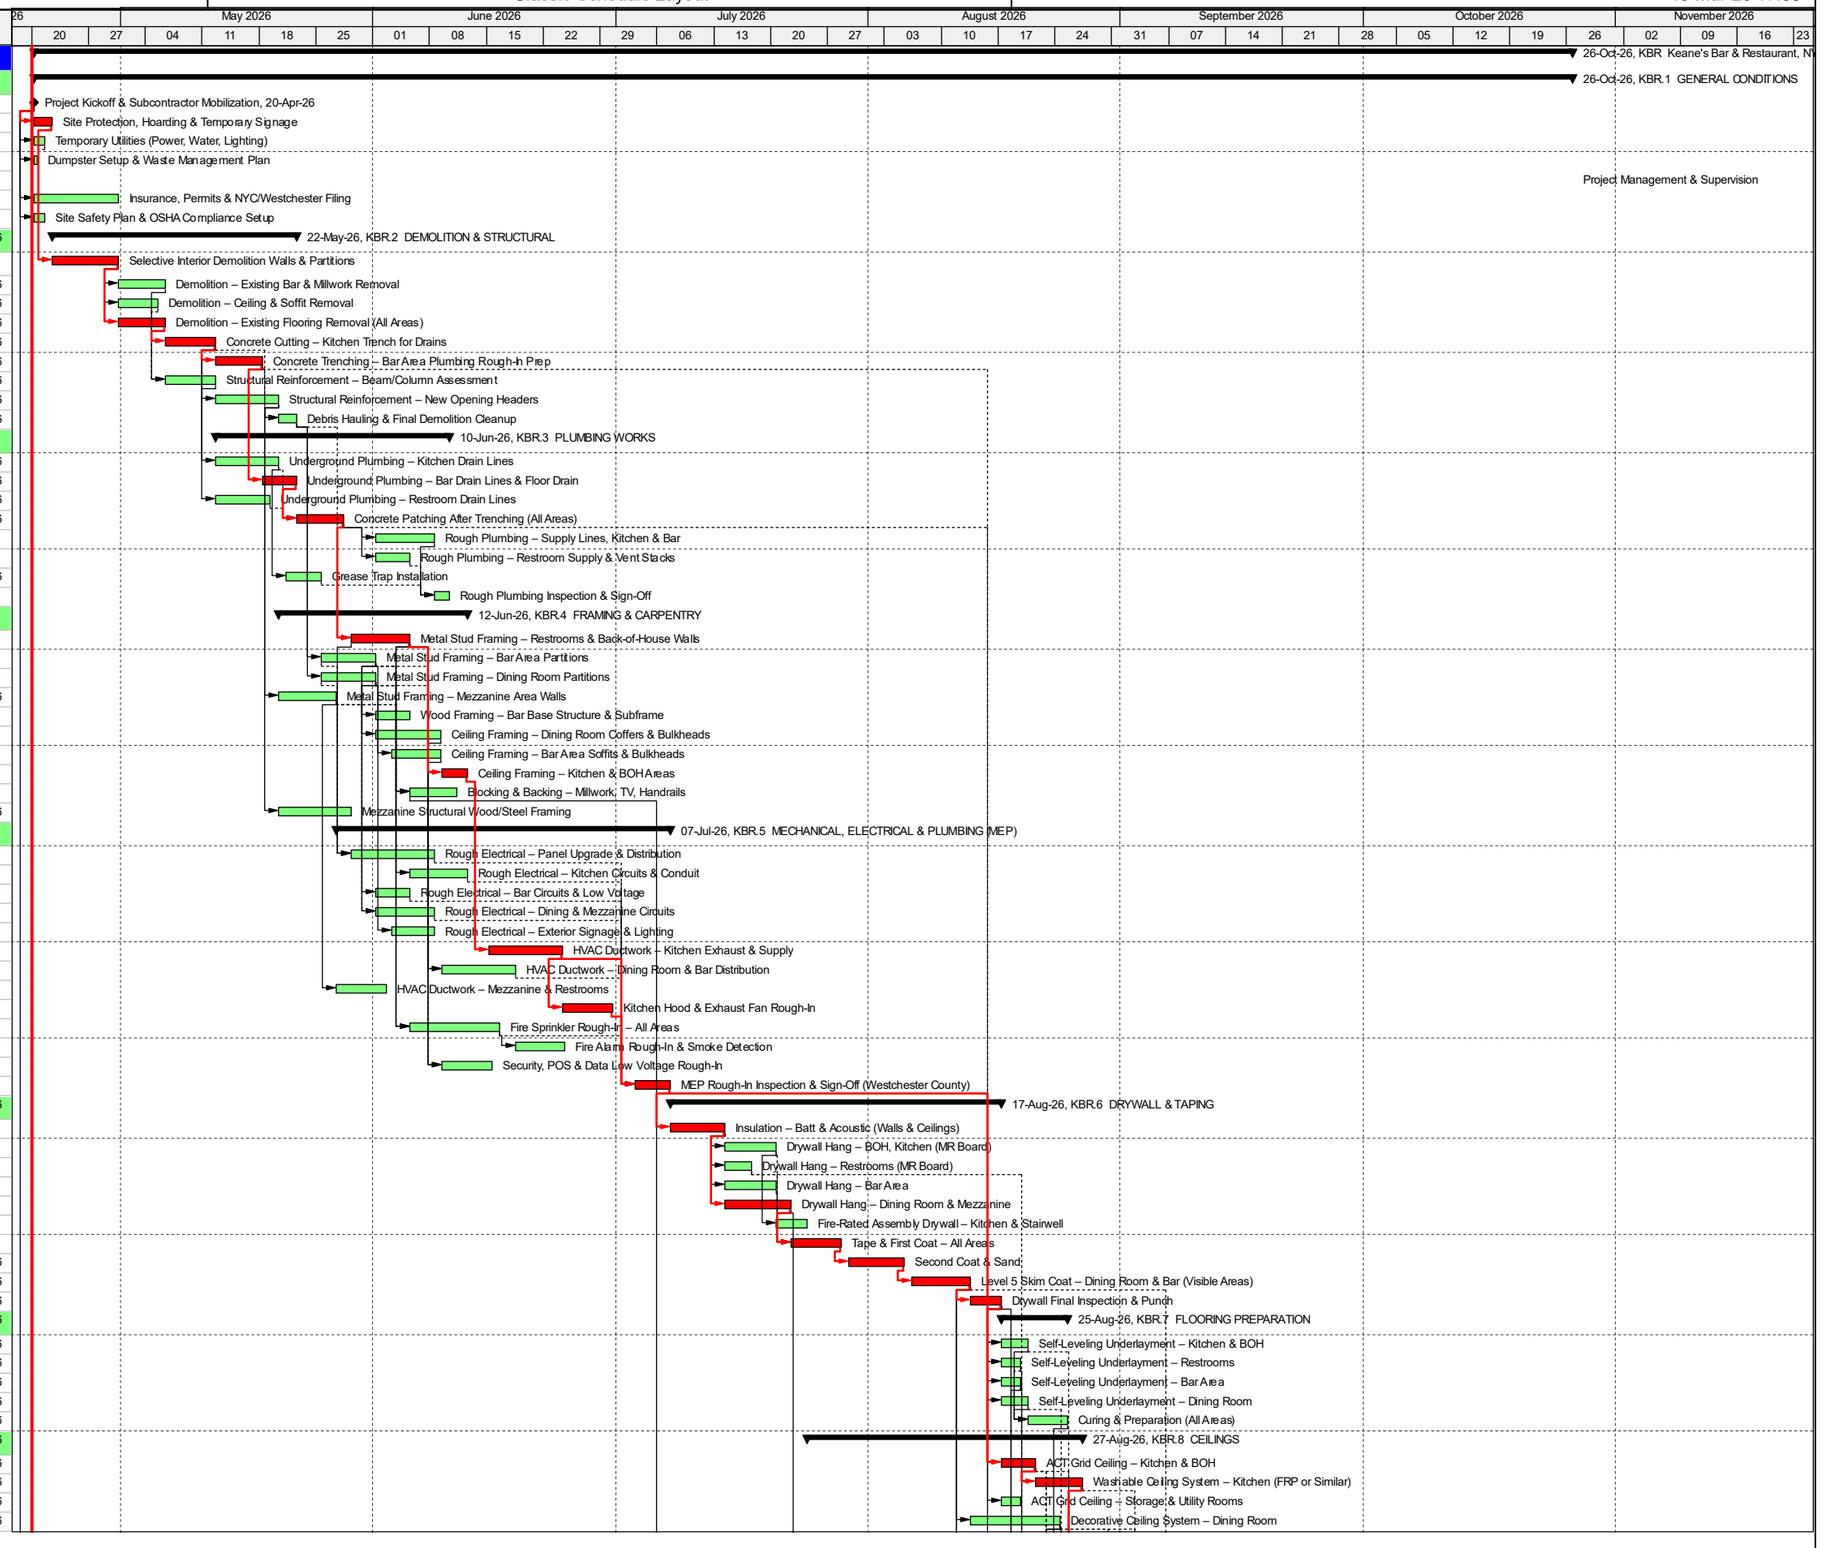


Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation

Activity ID	Activity Name	Original Duration	Start	Finish
A1650	Decorative Ceiling System – Bar Area	5	13-Aug-26	20-Aug-26
A1660	Bulkhead Finishing – All Areas	4	13-Aug-26	19-Aug-26
A1670	Mezzanine Ceiling & Railing Surrounds	4	24-Jul-26	30-Jul-26
KBR.9 FINISH FLOORING		14	20-Aug-26	10-Sep-26
A1680	Kitchen & BOH Tile Installation	6	27-Aug-26	04-Sep-26
A1690	Restroom Tile – Floor & Wainscot	5	21-Aug-26	31-Aug-26
A1700	Bar Area Stone / Tile Installation	5	20-Aug-26	27-Aug-26
A1710	Dining Room Hardwood Flooring Installation	6	26-Aug-26	04-Sep-26
A1720	Mezzanine Hardwood Flooring	4	25-Aug-26	31-Aug-26
A1730	Flooring Grout, Seal & Protection	3	04-Sep-26	10-Sep-26
KBR.10 FOH ARCHITECTURAL MILLWORK & B		98	20-Apr-26	18-Sep-26
A1740	Main Bar Fabrication (Shop Drawings & Fab)	24	20-Apr-26	26-May-26
A1750	Main Bar Installation – Base & Structure	5	27-Aug-26	03-Sep-26
A1760	Bar Top Installation – Stone / Solid Surface	3	04-Sep-26	10-Sep-26
A1770	Back Bar Display Unit & Shelving Installation	4	03-Sep-26	10-Sep-26
A1780	Keg Room Built-Ins & Storage Shelving	3	20-Aug-26	25-Aug-26
A1790	Banquette / Fixed Booth Seating Fabrication (C	20	07-Jul-26	07-Aug-26
A1800	Banquette / Booth Installation – Dining Room	4	04-Sep-26	10-Sep-26
A1810	Wine Wall & Display Cabinetry Installation	5	08-Sep-26	15-Sep-26
A1820	Host Stand Fabrication & Installation	3	13-Aug-26	19-Aug-26
A1830	Mezzanine Railing & Millwork	5	01-Sep-26	08-Sep-26
A1840	Millwork Punch & Touch-Up	2	15-Sep-26	18-Sep-26
KBR.11 FINISH MECHANICAL, ELECTRICAL & F		99	20-Apr-26	21-Sep-26
A1850	Kitchen Equipment Rough-In Connections (Gas	5	04-Sep-26	11-Sep-26
A1860	Bar Equipment Connections (Ice Tub, U/C Refs,	4	03-Sep-26	10-Sep-26
A1870	Restroom Fixture Installation (WC, Sinks, Acces	3	31-Aug-26	03-Sep-26
A1880	HVAC Equipment Installation – RTUs / AHUs	5	24-Aug-26	31-Aug-26
A1890	HVAC Diffusers, Grilles & Final Connections	3	01-Sep-26	04-Sep-26
A1900	Kitchen Hood Final Connection & Test	2	11-Sep-26	16-Sep-26
A1910	Electrical Devices & Trim (Outlets, Switches, Pla	4	04-Sep-26	10-Sep-26
A1920	Lighting Fixture Installation – Dining & Bar	5	24-Aug-26	31-Aug-26
A1930	Lighting Fixture Installation – Kitchen & BOH	2	27-Aug-26	31-Aug-26
A1940	Exterior Signage & Façade Lighting Installation	4	20-Aug-26	27-Aug-26
A1950	Fire Sprinkler Heads & Final Trim	2	24-Aug-26	27-Aug-26
A1960	Fire Alarm Devices, Horn/Strobe & Panel Progra	3	27-Aug-26	01-Sep-26
A1970	POS System, AV & Data Cabling Termination	4	20-Apr-26	24-Apr-26
A1980	MEP Final Inspection – Westchester County	2	16-Sep-26	21-Sep-26
KBR.12 PAINTING & WALL FINISHES		25	17-Aug-26	23-Sep-26
A1990	Prime Coat – All Drywall Areas	3	17-Aug-26	20-Aug-26
A2000	Paint – First Finish Coat BOH & Restrooms	3	03-Sep-26	09-Sep-26
A2010	Paint – First Finish Coat Bar & Dining	4	20-Aug-26	27-Aug-26
A2020	Specialty Wall Finish / Accent Walls – Dining & I	5	27-Aug-26	03-Sep-26
A2030	Paint – Final Touch-Up Coat (All Areas)	3	18-Sep-26	23-Sep-26
A2040	Exterior Paint / Sealant Touch-Up	2	27-Aug-26	31-Aug-26
KBR.13 SPECIALTIES & ACCESSORIES		19	27-Aug-26	25-Sep-26
A2050	Restroom Accessories (TP holders, soap, mirror	2	09-Sep-26	11-Sep-26
A2060	Kitchen Stainless Steel Shelving & Pass Shelf	3	11-Sep-26	17-Sep-26
A2070	Walk-In Cooler / Keg Room Installation	5	08-Sep-26	15-Sep-26
A2080	Fire Extinguisher & Hood Suppression System I	2	16-Sep-26	21-Sep-26
A2090	ADA Signage, Wayfinding & Exit Signs	2	23-Sep-26	25-Sep-26
A2100	Window Treatment / Blinds Installation	2	27-Aug-26	31-Aug-26
A2110	Exterior Entrance Matting & Thresholds	2	04-Sep-26	08-Sep-26
KBR.14 KITCHEN EQUIPMENT INSTALLATION		10	15-Sep-26	30-Sep-26
A2120	Kitchen Equipment Delivery & Setting	4	15-Sep-26	22-Sep-26
A2130	Equipment Final Connections & Commissioning	3	22-Sep-26	25-Sep-26
A2140	Hood Balancing & Kitchen Ventilation Test	2	25-Sep-26	29-Sep-26
A2150	Health Department Pre-Inspection Walkthrough	1	29-Sep-26	30-Sep-26
KBR.15 INSPECTIONS, CLOSEOUT & COMMIS		23	21-Sep-26	26-Oct-26
A2160	Building Department Final Inspection	2	25-Sep-26	29-Sep-26
A2170	Fire Department Inspection & Approval	2	21-Sep-26	22-Sep-26
A2180	Health Department Final Inspection	1	30-Sep-26	01-Oct-26
A2190	17-Sep-26	2	29-Sep-26	02-Oct-26
A2200	Electrical Load Test & Panel Sign-Off	2	21-Sep-26	22-Sep-26
A2210	Substantial Completion Walkthrough	1	01-Oct-26	02-Oct-26
A2220	Punch List Compilation	2	02-Oct-26	05-Oct-26
A2230	Punch List Execution	6	05-Oct-26	14-Oct-26
A2240	Final Cleaning – Deep Clean All Areas	2	14-Oct-26	16-Oct-26
A2250	Owner Training – Equipment & Systems	2	16-Oct-26	20-Oct-26
A2260	Certificate of Occupancy Received	1	01-Oct-26	02-Oct-26
A2270	Project Closeout – As-Builts, O&M Manuals, Wa	4	20-Oct-26	26-Oct-26
A2280	SUBSTANTIAL COMPLETION MILESTONE	0		16-Oct-26
A2290	PROJECT COMPLETE MILESTONE	0		26-Oct-26

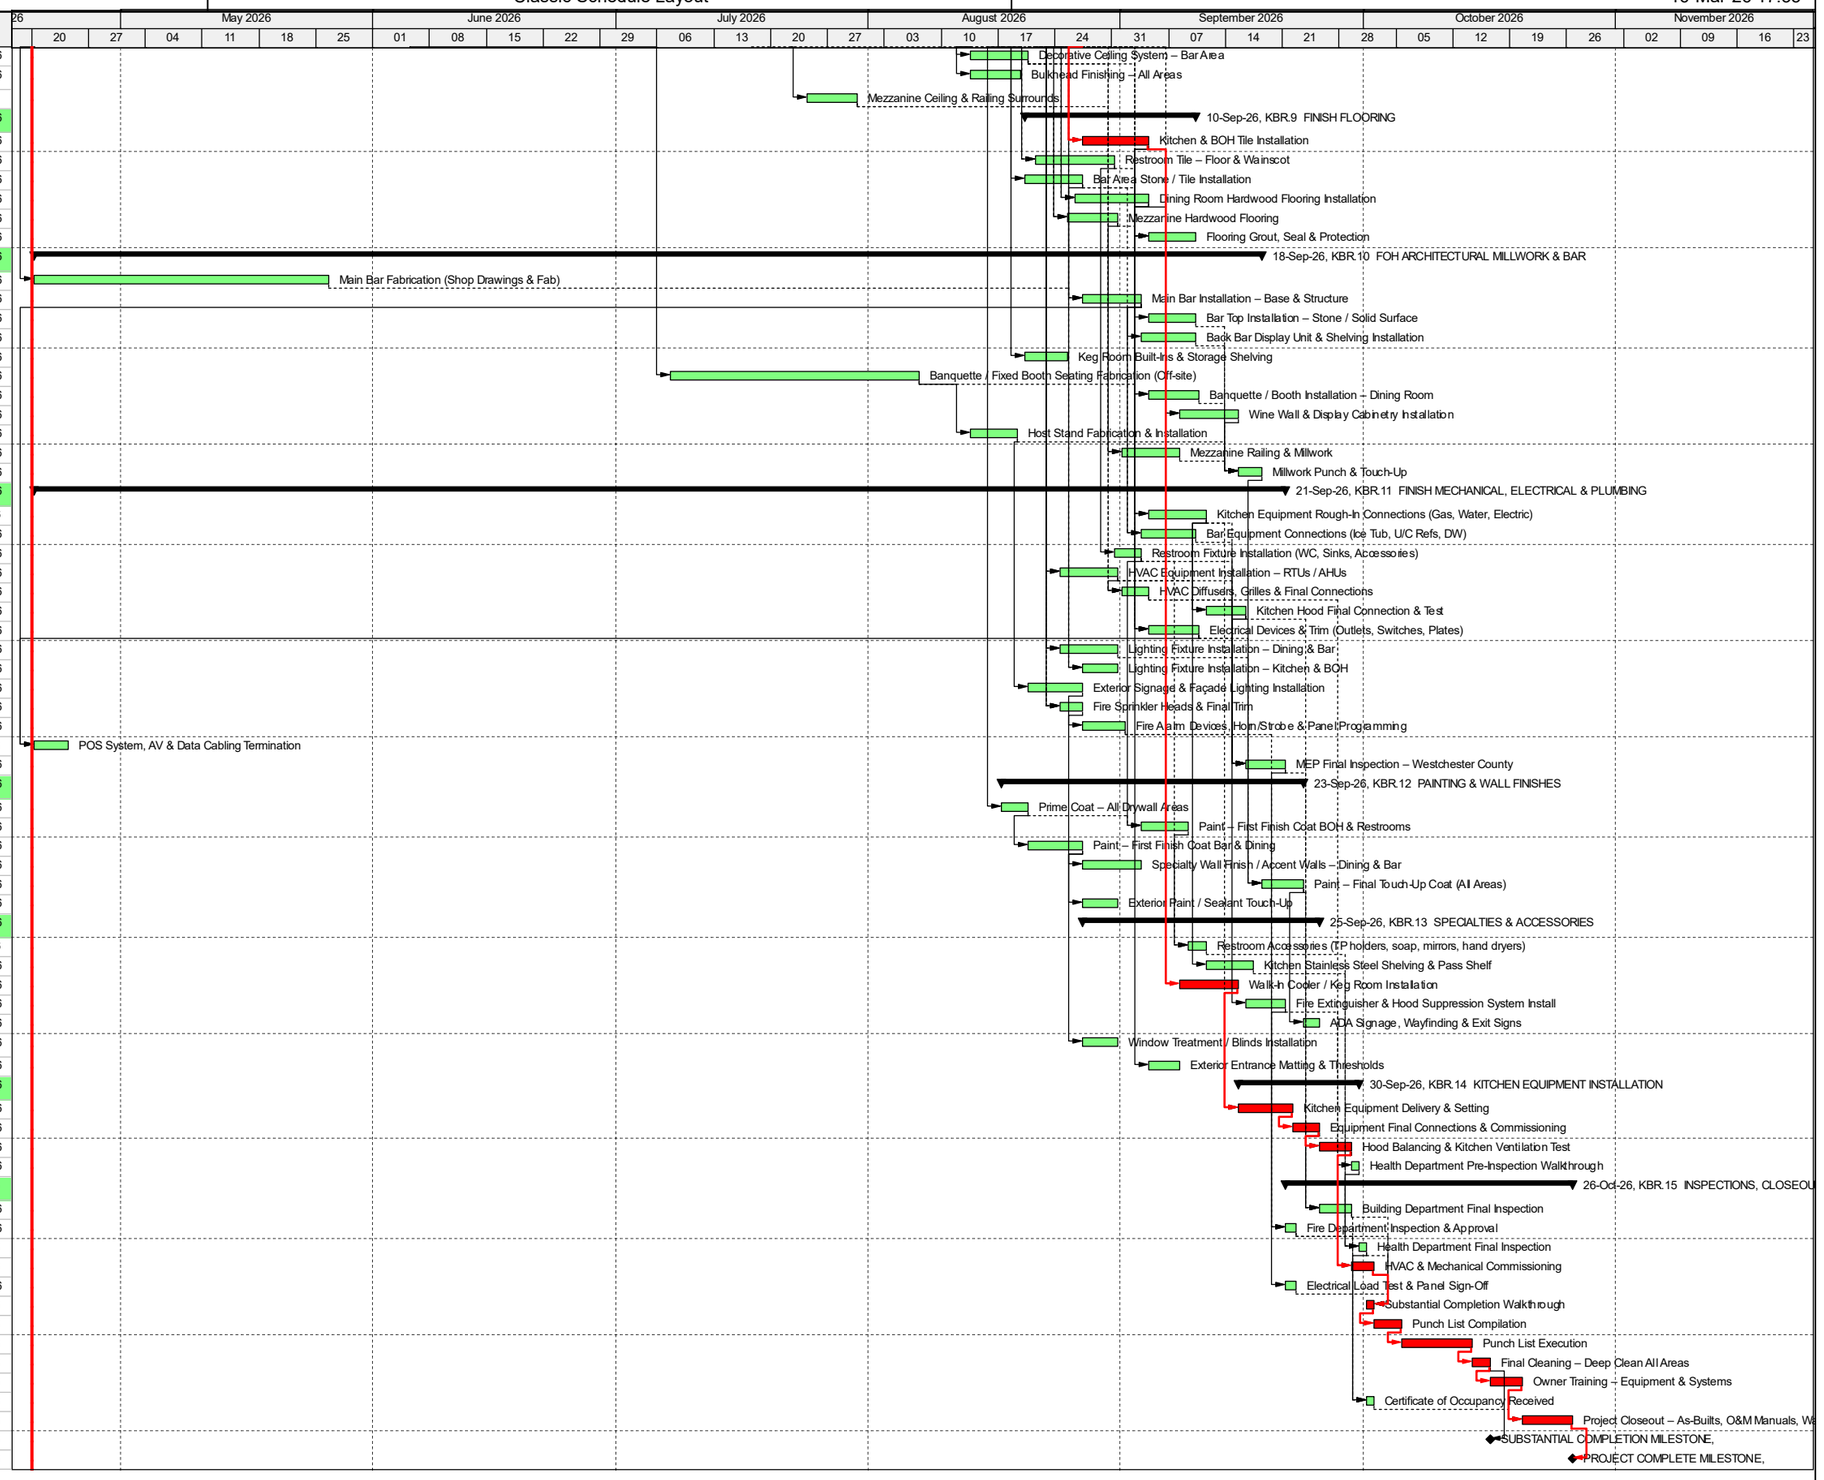

Actual Level of Effort | Actual Work | Remaining Work | Critical Remaining Work | Milestone | summary

TASK filter: All Activities

© Oracle Corporation
