
| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| LAB CEP | CEM LAB CEP 7112,7104,7135 | 1300 | 18-Aug-22 A | 12-Oct-26 | 18-Aug-22 | 07-Oct-25 |
| LAB CEP.PHASE1 | PRE-CONSTRUCTION: ENGINEER | 126 | 18-Aug-22 A | 11-Jan-23 A | 18-Aug-22 | 11-Jan-23 |
| LAB CEP.PHASE1.PC | PRE-CONSTRUCTION | 78 | 18-Aug-22 A | 16-Nov-22 A | 18-Aug-22 | 16-Nov-22 |
| A1000 | Architectural Conceptual Design & Masterplan | 15 | 18-Aug-22 A | 03-Sep-22 A | 18-Aug-22 | 03-Sep-22 |
| A1010 | Architectural Detailed Working Drawings | 20 | 05-Sep-22 A | 27-Sep-22 A | 05-Sep-22 | 27-Sep-22 |
| A1020 | Structural Design & Analysis Foundation (Raft) | 20 | 28-Sep-22 A | 20-Oct-22 A | 28-Sep-22 | 20-Oct-22 |
| A1030 | Structural Design & Analysis Superstructure (Frame) | 15 | 21-Oct-22 A | 07-Nov-22 A | 21-Oct-22 | 07-Nov-22 |
| A1040 | MEP Design HVAC System Drawings | 15 | 21-Oct-22 A | 07-Nov-22 A | 21-Oct-22 | 07-Nov-22 |
| A1050 | MEP Design Electrical System & Load Calculations | 15 | 21-Oct-22 A | 07-Nov-22 A | 21-Oct-22 | 07-Nov-22 |
| A1060 | MEP Design Plumbing, Drainage & Fire Fighting | 15 | 21-Oct-22 A | 07-Nov-22 A | 21-Oct-22 | 07-Nov-22 |
| A1070 | Facade, Shop Drawings & Coordination (BIM Clash Detection) | 8 | 08-Nov-22 A | 16-Nov-22 A | 08-Nov-22 | 16-Nov-22 |
| LAB CEP.PHASE1.LDA | LDA APPROVAL | 38 | 17-Nov-22 A | 30-Dec-22 A | 17-Nov-22 | 30-Dec-22 |
| A1080 | Building Plan Submission Lahore Development Authority (LDA | 5 | 17-Nov-22 A | 22-Nov-22 A | 17-Nov-22 | 22-Nov-22 |
| A1090 | LDA Review Period & Query Response | 15 | 23-Nov-22 A | 09-Dec-22 A | 23-Nov-22 | 09-Dec-22 |
| A1100 | LDA Building Plan Sanction (Approval Letter Received) | 8 | 10-Dec-22 A | 19-Dec-22 A | 10-Dec-22 | 19-Dec-22 |
| A1110 | NOC from WASA (Water & Sanitation Agency) | 10 | 20-Dec-22 A | 30-Dec-22 A | 20-Dec-22 | 30-Dec-22 |
| A1120 | NOC from LESCO (Electrical Connection) | 10 | 20-Dec-22 A | 30-Dec-22 A | 20-Dec-22 | 30-Dec-22 |
| A1130 | NOC from SNGPL (Gas Connection) | 9 | 20-Dec-22 A | 29-Dec-22 A | 20-Dec-22 | 29-Dec-22 |
| A1140 | Fire Department NOC | 10 | 20-Dec-22 A | 30-Dec-22 A | 20-Dec-22 | 30-Dec-22 |
| LAB CEP.PHASE1.PR | PROCUREMENT | 15 | 20-Dec-22 A | 05-Jan-23 A | 20-Dec-22 | 05-Jan-23 |
| A1150 | Procurement of Cement (Bulk Long-Term Supply Agreement) | 8 | 20-Dec-22 A | 28-Dec-22 A | 20-Dec-22 | 28-Dec-22 |
| A1160 | Procurement of Steel Reinforcement (4,000 Tons Whole Buildi | 8 | 20-Dec-22 A | 28-Dec-22 A | 20-Dec-22 | 28-Dec-22 |
| A1170 | Procurement of Formwork & Scaffolding System | 8 | 20-Dec-22 A | 28-Dec-22 A | 20-Dec-22 | 28-Dec-22 |
| A1180 | Procurement Tower Cranes (2 No.), Concrete Pumps & Transit | 8 | 20-Dec-22 A | 28-Dec-22 A | 20-Dec-22 | 28-Dec-22 |
| A1190 | Procurement MEP Long-Lead Items (Lifts, Transformers, Chille | 15 | 20-Dec-22 A | 05-Jan-23 A | 20-Dec-22 | 05-Jan-23 |
| LAB CEP.PHASE1.SM | SITE MOBILIZATION | 18 | 22-Dec-22 A | 11-Jan-23 A | 22-Dec-22 | 11-Jan-23 |
| A1200 | Site Boundary Wall, Hoarding & Security Fencing | 8 | 22-Dec-22 A | 31-Dec-22 A | 22-Dec-22 | 31-Dec-22 |
| A1210 | Site Office, Store Rooms & Labour Camp Setup | 8 | 31-Dec-22 A | 10-Jan-23 A | 31-Dec-22 | 10-Jan-23 |
| A1220 | Temporary Utilities Water Supply & Temporary Power | 5 | 31-Dec-22 A | 06-Jan-23 A | 31-Dec-22 | 06-Jan-23 |
| A1230 | Dewatering System Installation (Wellpoints / Submersible Pum | 5 | 31-Dec-22 A | 06-Jan-23 A | 31-Dec-22 | 06-Jan-23 |
| A1240 | Tower Crane Erection & Commissioning (2 No.) | 12 | 29-Dec-22 A | 11-Jan-23 A | 29-Dec-22 | 11-Jan-23 |
| LAB CEP.PHASE2 | CONSTRUCTION: STRUCTURAL & | 1094 | 12-Jan-23 A | 10-Jul-26 | 12-Jan-23 | 04-Aug-25 |
| LAB CEP.PHASE2.RAF | RAFT FOUNDATION | 293 | 12-Jan-23 A | 20-Dec-23 A | 12-Jan-23 | 03-Aug-23 |
| A1250 | Bulk Excavation for Raft Foundation | 12 | 12-Jan-23 A | 26-Jun-23 A | 12-Jan-23 | 25-Jan-23 |
| A1260 | Backfilling & Compaction of Raft Zone | 12 | 26-Jun-23 A | 08-Jul-23 A | 26-Jan-23 | 08-Feb-23 |
| A1270 | Pre-Construction Anti-Termite Treatment | 13 | 08-Jul-23 A | 22-Jul-23 A | 09-Feb-23 | 23-Feb-23 |
| A1280 | PCC Blinding Layer Raft | 13 | 22-Jul-23 A | 05-Aug-23 A | 24-Feb-23 | 10-Mar-23 |
| A1290 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 4 | 05-Aug-23 A | 09-Aug-23 A | 11-Mar-23 | 15-Mar-23 |
| A1300 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 15 | 09-Aug-23 A | 25-Aug-23 A | 16-Mar-23 | 01-Apr-23 |
| A1310 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 8 | 25-Aug-23 A | 02-Sep-23 A | 03-Apr-23 | 11-Apr-23 |
| A1320 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 02-Sep-23 A | 09-Sep-23 A | 12-Apr-23 | 19-Apr-23 |
| A1330 | Formwork Stripping & Removal Section 1/4 | 2 | 09-Sep-23 A | 11-Sep-23 A | 20-Apr-23 | 21-Apr-23 |
| A1340 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 4 | 04-Sep-23 A | 08-Sep-23 A | 13-Apr-23 | 18-Apr-23 |
| A1350 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 14 | 08-Sep-23 A | 23-Sep-23 A | 18-Apr-23 | 04-May-23 |
| A1360 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 8 | 23-Sep-23 A | 02-Oct-23 A | 04-May-23 | 13-May-23 |
| A1370 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 02-Oct-23 A | 09-Oct-23 A | 13-May-23 | 22-May-23 |
| A1380 | Formwork Stripping & Removal Section 2/4 | 2 | 09-Oct-23 A | 10-Oct-23 A | 22-May-23 | 24-May-23 |
| A1390 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 4 | 03-Oct-23 A | 07-Oct-23 A | 15-May-23 | 19-May-23 |
| A1400 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 16 | 07-Oct-23 A | 25-Oct-23 A | 19-May-23 | 07-Jun-23 |
| A1410 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 9 | 25-Oct-23 A | 03-Nov-23 A | 07-Jun-23 | 17-Jun-23 |
| A1420 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 03-Nov-23 A | 10-Nov-23 A | 17-Jun-23 | 26-Jun-23 |
| A1430 | Formwork Stripping & Removal Section 3/4 | 2 | 10-Nov-23 A | 11-Nov-23 A | 26-Jun-23 | 28-Jun-23 |
| A1100 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 4 | 04-Nov-23 A | 09-Nov-23 A | 19-Jun-23 | 23-Jun-23 |
| A1450 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 17 | 09-Nov-23 A | 29-Nov-23 A | 23-Jun-23 | 13-Jul-23 |
| A1460 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 9 | 29-Nov-23 A | 09-Dec-23 A | 13-Jul-23 | 24-Jul-23 |
| A1470 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 09-Dec-23 A | 18-Dec-23 A | 24-Jul-23 | 01-Aug-23 |
| A1480 | Formwork Stripping & Removal Section 4/4 | 2 | 18-Dec-23 A | 20-Dec-23 A | 01-Aug-23 | 03-Aug-23 |
| LAB CEP.PHASE2.B4 | BASEMENT-04 | 136 | 11-Sep-23 A | 16-Feb-24 A | 22-Apr-23 | 24-Nov-23 |
| A1490 | PCC Blinding Layer Basement-04 | 23 | 11-Sep-23 A | 06-Oct-23 A | 22-Apr-23 | 18-May-23 |
| A1500 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 7 | 11-Sep-23 A | 18-Sep-23 A | 22-Apr-23 | 29-Apr-23 |
| A1510 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 4 | 18-Sep-23 A | 21-Sep-23 A | 01-May-23 | 04-May-23 |
| A1520 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 2 | 21-Sep-23 A | 22-Sep-23 A | 05-May-23 | 06-May-23 |
| A1530 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 22-Sep-23 A | 29-Sep-23 A | 08-May-23 | 15-May-23 |





Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone

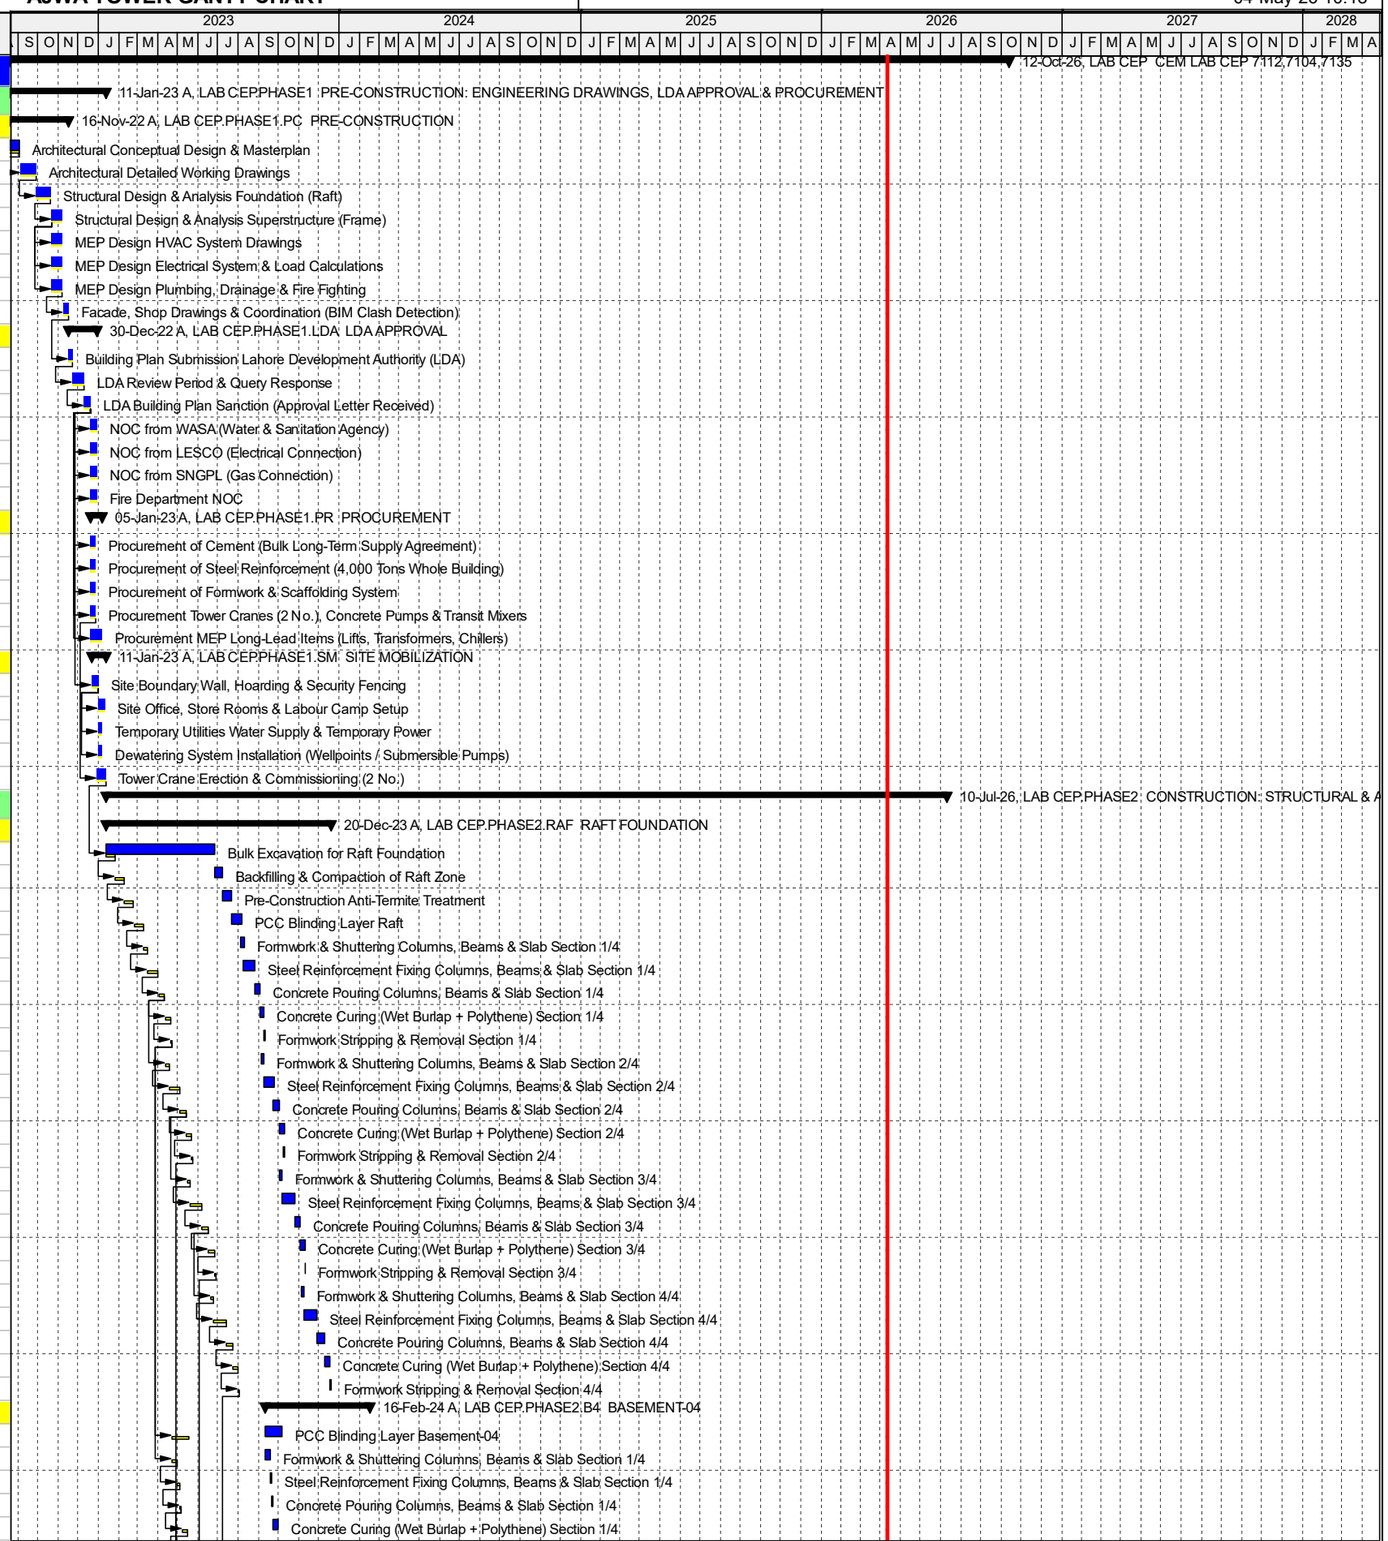

TASK filter: All Activities

© Oracle Corporation


| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A1540 | Formwork Stripping & Removal Section 1/4 | 2 | 29-Sep-23 A | 30-Sep-23 A | 16-May-23 | 17-May-23 |
| A1550 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 23-Sep-23 A | 30-Sep-23 A | 24-May-23 | 31-May-23 |
| A1560 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 5 | 30-Sep-23 A | 06-Oct-23 A | 31-May-23 | 06-Jun-23 |
| A1570 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 06-Oct-23 A | 09-Oct-23 A | 06-Jun-23 | 08-Jun-23 |
| A1580 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 09-Oct-23 A | 17-Oct-23 A | 08-Jun-23 | 16-Jun-23 |
| A1590 | Formwork Stripping & Removal Section 2/4 | 2 | 17-Oct-23 A | 19-Oct-23 A | 16-Jun-23 | 19-Jun-23 |
| A1600 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 7 | 10-Oct-23 A | 18-Oct-23 A | 28-Jun-23 | 06-Jul-23 |
| A1610 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 4 | 18-Oct-23 A | 23-Oct-23 A | 06-Jul-23 | 11-Jul-23 |
| A1620 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 23-Oct-23 A | 25-Oct-23 A | 11-Jul-23 | 13-Jul-23 |
| A1630 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 25-Oct-23 A | 02-Nov-23 A | 14-Jul-23 | 21-Jul-23 |
| A1640 | Formwork Stripping & Removal Section 3/4 | 2 | 02-Nov-23 A | 04-Nov-23 A | 22-Jul-23 | 24-Jul-23 |
| A1650 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 8 | 26-Oct-23 A | 03-Nov-23 A | 03-Aug-23 | 12-Aug-23 |
| A1660 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 5 | 03-Nov-23 A | 09-Nov-23 A | 12-Aug-23 | 18-Aug-23 |
| A1670 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 09-Nov-23 A | 13-Nov-23 A | 18-Aug-23 | 21-Aug-23 |
| A1680 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 13-Nov-23 A | 21-Nov-23 A | 21-Aug-23 | 29-Aug-23 |
| A1690 | Formwork Stripping & Removal Section 4/4 | 3 | 21-Nov-23 A | 23-Nov-23 A | 29-Aug-23 | 01-Sep-23 |
| A1700 | Brickwork & Masonry Partition Walls Basement-04 | 8 | 23-Nov-23 A | 02-Dec-23 A | 01-Sep-23 | 09-Sep-23 |
| A1710 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Base | 35 | 02-Dec-23 A | 12-Jan-24 A | 09-Sep-23 | 20-Oct-23 |
| A1720 | Floor Finishes (Tiles/Marble/Screed) Basement-04 [Basement ( | 30 | 12-Jan-24 A | 16-Feb-24 A | 20-Oct-23 | 24-Nov-23 |
| **LAB CEP.PHASE2.B3 BASEMENT-03** | | 99 | 30-Sep-23 A | 24-Jan-24 A | 18-May-23 | 08-Nov-23 |
| A1730 | PCC Blinding Layer Basement-03 | 24 | 30-Sep-23 A | 27-Oct-23 A | 18-May-23 | 14-Jun-23 |
| A1740 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 7 | 30-Sep-23 A | 07-Oct-23 A | 18-May-23 | 25-May-23 |
| A1750 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 4 | 07-Oct-23 A | 11-Oct-23 A | 26-May-23 | 30-May-23 |
| A1760 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 11-Oct-23 A | 13-Oct-23 A | 31-May-23 | 02-Jun-23 |
| A1770 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 13-Oct-23 A | 21-Oct-23 A | 02-Jun-23 | 10-Jun-23 |
| A1780 | Formwork Stripping & Removal Section 1/4 | 2 | 21-Oct-23 A | 24-Oct-23 A | 10-Jun-23 | 13-Jun-23 |
| A1790 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 7 | 14-Oct-23 A | 23-Oct-23 A | 19-Jun-23 | 27-Jun-23 |
| A1800 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 4 | 23-Oct-23 A | 27-Oct-23 A | 27-Jun-23 | 01-Jul-23 |
| A1810 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 27-Oct-23 A | 31-Oct-23 A | 01-Jul-23 | 05-Jul-23 |
| A1820 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 31-Oct-23 A | 08-Nov-23 A | 05-Jul-23 | 13-Jul-23 |
| A1830 | Formwork Stripping & Removal Section 2/4 | 2 | 08-Nov-23 A | 10-Nov-23 A | 13-Jul-23 | 15-Jul-23 |
| A1840 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 7 | 01-Nov-23 A | 09-Nov-23 A | 25-Jul-23 | 01-Aug-23 |
| A1850 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 4 | 09-Nov-23 A | 14-Nov-23 A | 02-Aug-23 | 05-Aug-23 |
| A1860 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 14-Nov-23 A | 16-Nov-23 A | 07-Aug-23 | 09-Aug-23 |
| A1870 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 16-Nov-23 A | 24-Nov-23 A | 09-Aug-23 | 17-Aug-23 |
| A1880 | Formwork Stripping & Removal Section 3/4 | 3 | 24-Nov-23 A | 28-Nov-23 A | 17-Aug-23 | 19-Aug-23 |
| A1890 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 7 | 17-Nov-23 A | 25-Nov-23 A | 01-Sep-23 | 09-Sep-23 |
| A1900 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 4 | 25-Nov-23 A | 30-Nov-23 A | 09-Sep-23 | 14-Sep-23 |
| A1910 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 30-Nov-23 A | 02-Dec-23 A | 14-Sep-23 | 16-Sep-23 |
| A1920 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 02-Dec-23 A | 11-Dec-23 A | 16-Sep-23 | 25-Sep-23 |
| A1930 | Formwork Stripping & Removal Section 4/4 | 3 | 11-Dec-23 A | 14-Dec-23 A | 25-Sep-23 | 28-Sep-23 |
| A1940 | Brickwork & Masonry Partition Walls Basement-03 | 5 | 14-Dec-23 A | 20-Dec-23 A | 28-Sep-23 | 04-Oct-23 |
| A1950 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Base | 10 | 20-Dec-23 A | 01-Jan-24 A | 04-Oct-23 | 16-Oct-23 |
| A1960 | Floor Finishes (Tiles/Marble/Screed) Basement-03 [Basement ( | 20 | 01-Jan-24 A | 24-Jan-24 A | 16-Oct-23 | 08-Nov-23 |
| **LAB CEP.PHASE2.B2 BASEMENT-02** | | 104 | 24-Oct-23 A | 21-Feb-24 A | 13-Jun-23 | 07-Dec-23 |
| A1970 | PCC Blinding Layer Basement-02 | 7 | 24-Oct-23 A | 31-Oct-23 A | 13-Jun-23 | 21-Jun-23 |
| A1980 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 8 | 24-Oct-23 A | 01-Nov-23 A | 13-Jun-23 | 21-Jun-23 |
| A1990 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 5 | 01-Nov-23 A | 07-Nov-23 A | 22-Jun-23 | 27-Jun-23 |
| A1100 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 07-Nov-23 A | 09-Nov-23 A | 28-Jun-23 | 30-Jun-23 |
| A2010 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 09-Nov-23 A | 16-Nov-23 A | 30-Jun-23 | 08-Jul-23 |
| A2020 | Formwork Stripping & Removal Section 1/4 | 3 | 16-Nov-23 A | 18-Nov-23 A | 08-Jul-23 | 11-Jul-23 |
| A2030 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 8 | 10-Nov-23 A | 18-Nov-23 A | 15-Jul-23 | 24-Jul-23 |
| A2040 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 5 | 18-Nov-23 A | 24-Nov-23 A | 24-Jul-23 | 29-Jul-23 |
| A2050 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 24-Nov-23 A | 28-Nov-23 A | 29-Jul-23 | 02-Aug-23 |
| A2060 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 28-Nov-23 A | 06-Dec-23 A | 02-Aug-23 | 10-Aug-23 |
| A2070 | Formwork Stripping & Removal Section 2/4 | 3 | 06-Dec-23 A | 08-Dec-23 A | 10-Aug-23 | 12-Aug-23 |
| A2080 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 8 | 29-Nov-23 A | 07-Dec-23 A | 21-Aug-23 | 29-Aug-23 |
| A2090 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 5 | 07-Dec-23 A | 12-Dec-23 A | 29-Aug-23 | 04-Sep-23 |
| A2100 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 12-Dec-23 A | 14-Dec-23 A | 04-Sep-23 | 06-Sep-23 |
| A2110 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 14-Dec-23 A | 22-Dec-23 A | 07-Sep-23 | 14-Sep-23 |
| A2120 | Formwork Stripping & Removal Section 3/4 | 3 | 22-Dec-23 A | 25-Dec-23 A | 15-Sep-23 | 18-Sep-23 |
| A2130 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 8 | 15-Dec-23 A | 23-Dec-23 A | 28-Sep-23 | 06-Oct-23 |
| A2140 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 5 | 23-Dec-23 A | 29-Dec-23 A | 06-Oct-23 | 12-Oct-23 |
| A2150 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 29-Dec-23 A | 01-Jan-24 A | 12-Oct-23 | 16-Oct-23 |

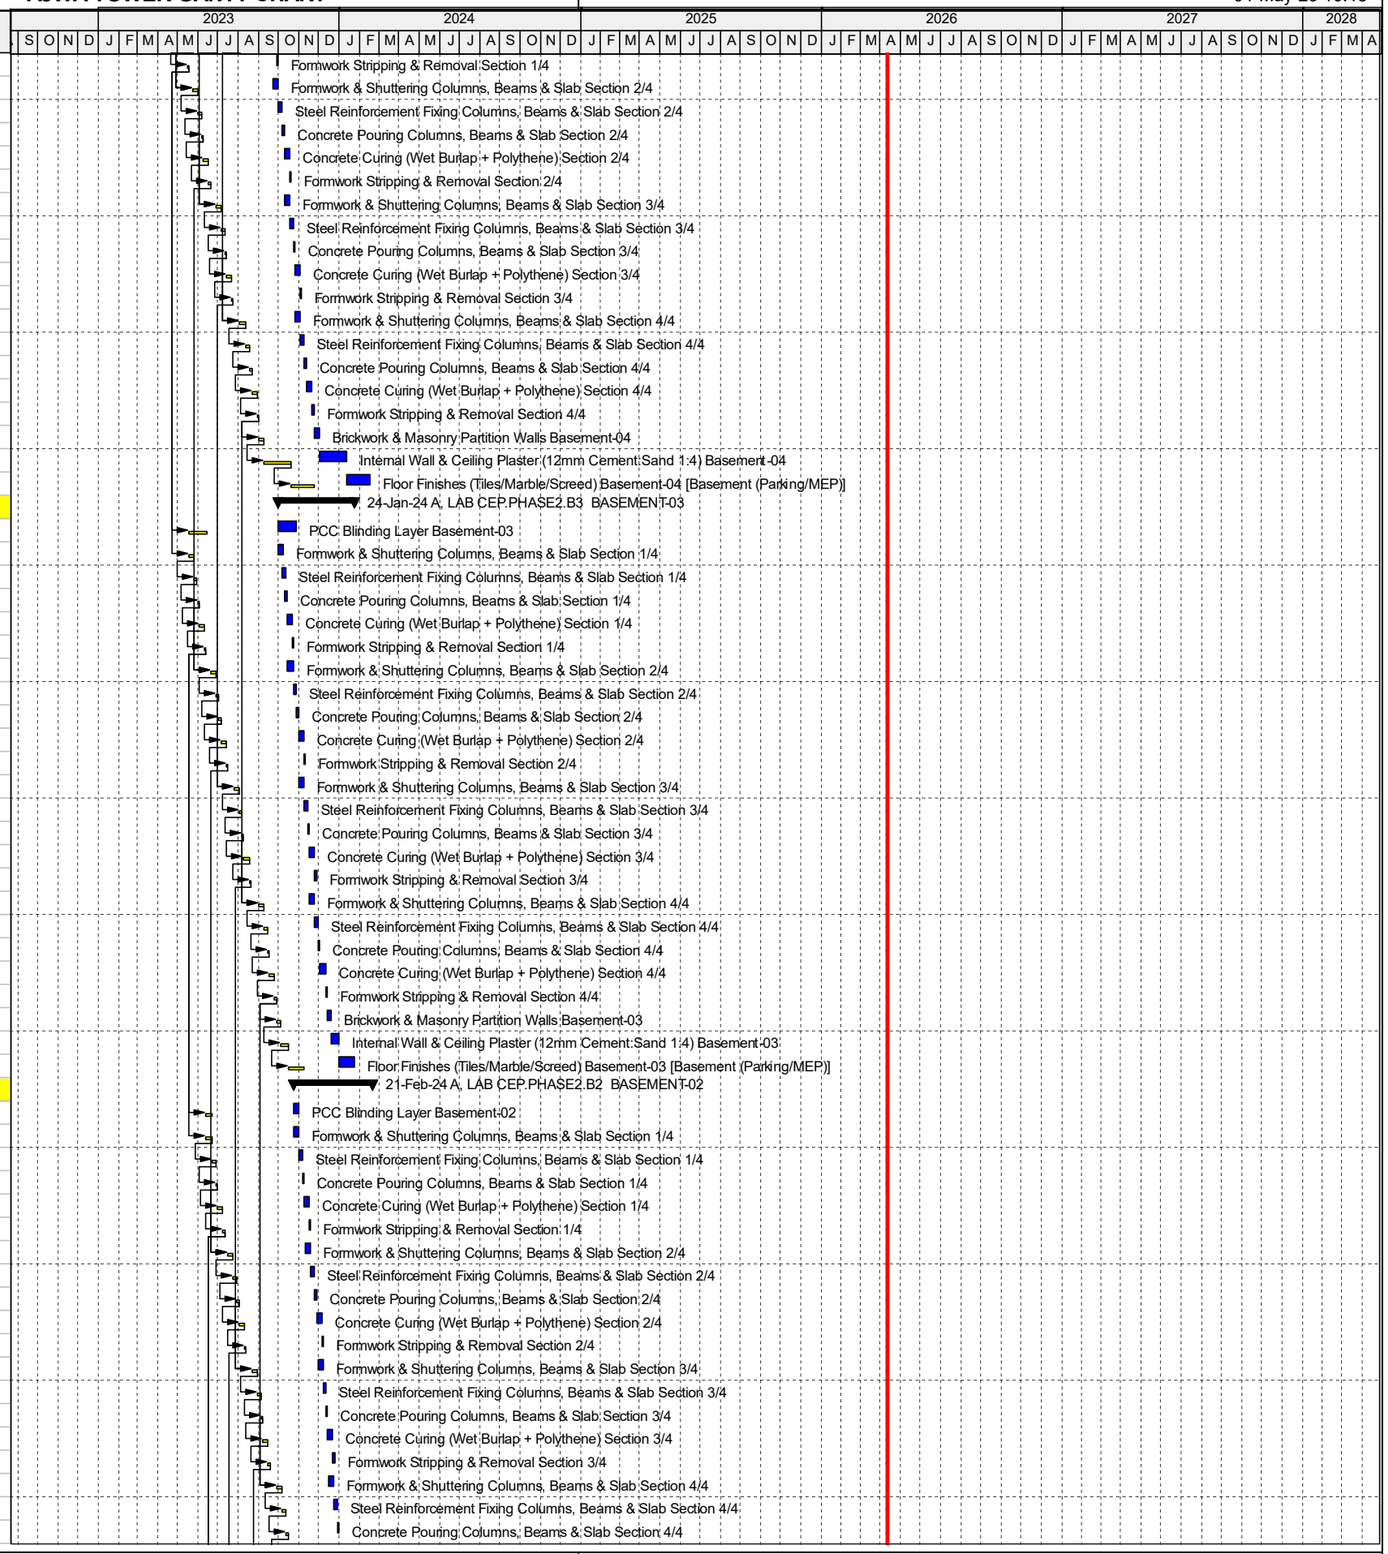




© Oracle Corporation


| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A2160 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 01-Jan-24 A | 08-Jan-24 A | 16-Oct-23 | 24-Oct-23 |
| A2170 | Formwork Stripping & Removal Section 4/4 | 3 | 08-Jan-24 A | 10-Jan-24 A | 24-Oct-23 | 26-Oct-23 |
| A2180 | Brickwork & Masonry Partition Walls Basement-02 | 6 | 10-Jan-24 A | 17-Jan-24 A | 26-Oct-23 | 02-Nov-23 |
| A2190 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Base | 10 | 17-Jan-24 A | 29-Jan-24 A | 03-Nov-23 | 14-Nov-23 |
| A2200 | Floor Finishes (Tiles/Marble/Screed) Basement-02 [Basement ( | 20 | 29-Jan-24 A | 21-Feb-24 A | 15-Nov-23 | 07-Dec-23 |
| **LAB CEP.PHASE2.B1 BASEMENT-01** | | 91 | 18-Nov-23 A | 12-Mar-24 A | 12-Jul-23 | 18-Jan-24 |
| A2210 | PCC Blinding Layer Basement-01 | 7 | 18-Nov-23 A | 25-Nov-23 A | 12-Jul-23 | 19-Jul-23 |
| A2220 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 8 | 18-Nov-23 A | 27-Nov-23 A | 12-Jul-23 | 20-Jul-23 |
| A2230 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 5 | 27-Nov-23 A | 02-Dec-23 A | 20-Jul-23 | 26-Jul-23 |
| A2240 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 02-Dec-23 A | 05-Dec-23 A | 26-Jul-23 | 28-Jul-23 |
| A2250 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 05-Dec-23 A | 12-Dec-23 A | 29-Jul-23 | 05-Aug-23 |
| A2260 | Formwork Stripping & Removal Section 1/4 | 3 | 12-Dec-23 A | 14-Dec-23 A | 07-Aug-23 | 09-Aug-23 |
| A2270 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 8 | 06-Dec-23 A | 14-Dec-23 A | 12-Aug-23 | 22-Aug-23 |
| A2280 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 5 | 14-Dec-23 A | 20-Dec-23 A | 22-Aug-23 | 28-Aug-23 |
| A2290 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 20-Dec-23 A | 23-Dec-23 A | 28-Aug-23 | 30-Aug-23 |
| A2300 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 23-Dec-23 A | 01-Jan-24 A | 30-Aug-23 | 07-Sep-23 |
| A2310 | Formwork Stripping & Removal Section 2/4 | 3 | 01-Jan-24 A | 03-Jan-24 A | 07-Sep-23 | 11-Sep-23 |
| A2320 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 8 | 25-Dec-23 A | 02-Jan-24 A | 18-Sep-23 | 26-Sep-23 |
| A2330 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 5 | 02-Jan-24 A | 08-Jan-24 A | 27-Sep-23 | 02-Oct-23 |
| A2340 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 08-Jan-24 A | 11-Jan-24 A | 03-Oct-23 | 05-Oct-23 |
| A2350 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 11-Jan-24 A | 19-Jan-24 A | 05-Oct-23 | 13-Oct-23 |
| A2360 | Formwork Stripping & Removal Section 3/4 | 3 | 19-Jan-24 A | 22-Jan-24 A | 13-Oct-23 | 16-Oct-23 |
| A2370 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 8 | 12-Jan-24 A | 20-Jan-24 A | 26-Oct-23 | 04-Nov-23 |
| A2380 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 5 | 20-Jan-24 A | 25-Jan-24 A | 04-Nov-23 | 10-Nov-23 |
| A2390 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 25-Jan-24 A | 27-Jan-24 A | 10-Nov-23 | 13-Nov-23 |
| A2400 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 27-Jan-24 A | 05-Feb-24 A | 13-Nov-23 | 21-Nov-23 |
| A2410 | Formwork Stripping & Removal Section 4/4 | 3 | 05-Feb-24 A | 07-Feb-24 A | 21-Nov-23 | 24-Nov-23 |
| A2420 | Brickwork & Masonry Partition Walls Basement-01 | 13 | 08-Jan-24 A | 22-Jan-24 A | 24-Nov-23 | 08-Dec-23 |
| A2430 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Base | 20 | 22-Jan-24 A | 14-Feb-24 A | 08-Dec-23 | 01-Jan-24 |
| A2440 | Floor Finishes (Tiles/Marble/Screed) Basement-01 [Basement ( | 15 | 14-Feb-24 A | 12-Mar-24 A | 01-Jan-24 | 18-Jan-24 |
| **LAB CEP.PHASE2.GF GROUND FLOOR** | | 155 | 14-Dec-23 A | 12-Jun-24 A | 09-Aug-23 | 17-Apr-24 |
| A2450 | PCC Blinding Layer Ground Floor | 8 | 14-Dec-23 A | 22-Dec-23 A | 09-Aug-23 | 17-Aug-23 |
| A2460 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 14-Dec-23 A | 19-Dec-23 A | 09-Aug-23 | 15-Aug-23 |
| A2470 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 19-Dec-23 A | 21-Dec-23 A | 15-Aug-23 | 17-Aug-23 |
| A2480 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 21-Dec-23 A | 23-Dec-23 A | 18-Aug-23 | 21-Aug-23 |
| A2490 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 23-Dec-23 A | 30-Dec-23 A | 21-Aug-23 | 29-Aug-23 |
| A2500 | Formwork Stripping & Removal Section 1/4 | 3 | 30-Dec-23 A | 02-Jan-24 A | 29-Aug-23 | 31-Aug-23 |
| A2510 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 5 | 25-Dec-23 A | 30-Dec-23 A | 11-Sep-23 | 16-Sep-23 |
| A2520 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 30-Dec-23 A | 02-Jan-24 A | 16-Sep-23 | 19-Sep-23 |
| A2530 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 02-Jan-24 A | 05-Jan-24 A | 19-Sep-23 | 22-Sep-23 |
| A2540 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 05-Jan-24 A | 13-Jan-24 A | 22-Sep-23 | 30-Sep-23 |
| A2550 | Formwork Stripping & Removal Section 2/4 | 3 | 13-Jan-24 A | 16-Jan-24 A | 30-Sep-23 | 03-Oct-23 |
| A2560 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 5 | 06-Jan-24 A | 12-Jan-24 A | 17-Oct-23 | 21-Oct-23 |
| A2570 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 12-Jan-24 A | 15-Jan-24 A | 23-Oct-23 | 25-Oct-23 |
| A2580 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 15-Jan-24 A | 17-Jan-24 A | 25-Oct-23 | 27-Oct-23 |
| A2590 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 17-Jan-24 A | 25-Jan-24 A | 28-Oct-23 | 04-Nov-23 |
| A2600 | Formwork Stripping & Removal Section 3/4 | 3 | 25-Jan-24 A | 27-Jan-24 A | 06-Nov-23 | 08-Nov-23 |
| A2610 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 5 | 18-Jan-24 A | 24-Jan-24 A | 24-Nov-23 | 30-Nov-23 |
| A2620 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 24-Jan-24 A | 27-Jan-24 A | 30-Nov-23 | 02-Dec-23 |
| A2630 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 27-Jan-24 A | 30-Jan-24 A | 02-Dec-23 | 06-Dec-23 |
| A2640 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 30-Jan-24 A | 07-Feb-24 A | 06-Dec-23 | 14-Dec-23 |
| A2650 | Formwork Stripping & Removal Section 4/4 | 3 | 07-Feb-24 A | 10-Feb-24 A | 14-Dec-23 | 16-Dec-23 |
| A2660 | Brickwork & Masonry Partition Walls Ground Floor | 30 | 10-Feb-24 A | 16-Mar-24 A | 16-Dec-23 | 20-Jan-24 |
| A2670 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Grou | 40 | 16-Mar-24 A | 02-May-24 A | 20-Jan-24 | 07-Mar-24 |
| A2680 | Floor Finishes (Tiles/Marble/Screed) Ground Floor [Basement (F | 35 | 02-May-24 A | 12-Jun-24 A | 07-Mar-24 | 17-Apr-24 |
| **LAB CEP.PHASE2.F1 1ST FLOOR SHOPPING MALL** | | 167 | 02-Jan-24 A | 13-Jul-24 A | 01-Sep-23 | 11-May-24 |
| A2690 | PCC Blinding Layer 1st Floor | 8 | 02-Jan-24 A | 10-Jan-24 A | 01-Sep-23 | 09-Sep-23 |
| A2700 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 02-Jan-24 A | 06-Jan-24 A | 01-Sep-23 | 06-Sep-23 |
| A1100 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 4 | 06-Jan-24 A | 10-Jan-24 A | 07-Sep-23 | 11-Sep-23 |
| A2720 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 10-Jan-24 A | 13-Jan-24 A | 11-Sep-23 | 14-Sep-23 |
| A2730 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 13-Jan-24 A | 22-Jan-24 A | 14-Sep-23 | 22-Sep-23 |
| A2740 | Formwork Stripping & Removal Section 1/4 | 3 | 22-Jan-24 A | 24-Jan-24 A | 22-Sep-23 | 25-Sep-23 |
| A2750 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 5 | 15-Jan-24 A | 20-Jan-24 A | 03-Oct-23 | 09-Oct-23 |
| A2760 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 4 | 20-Jan-24 A | 24-Jan-24 A | 09-Oct-23 | 13-Oct-23 |

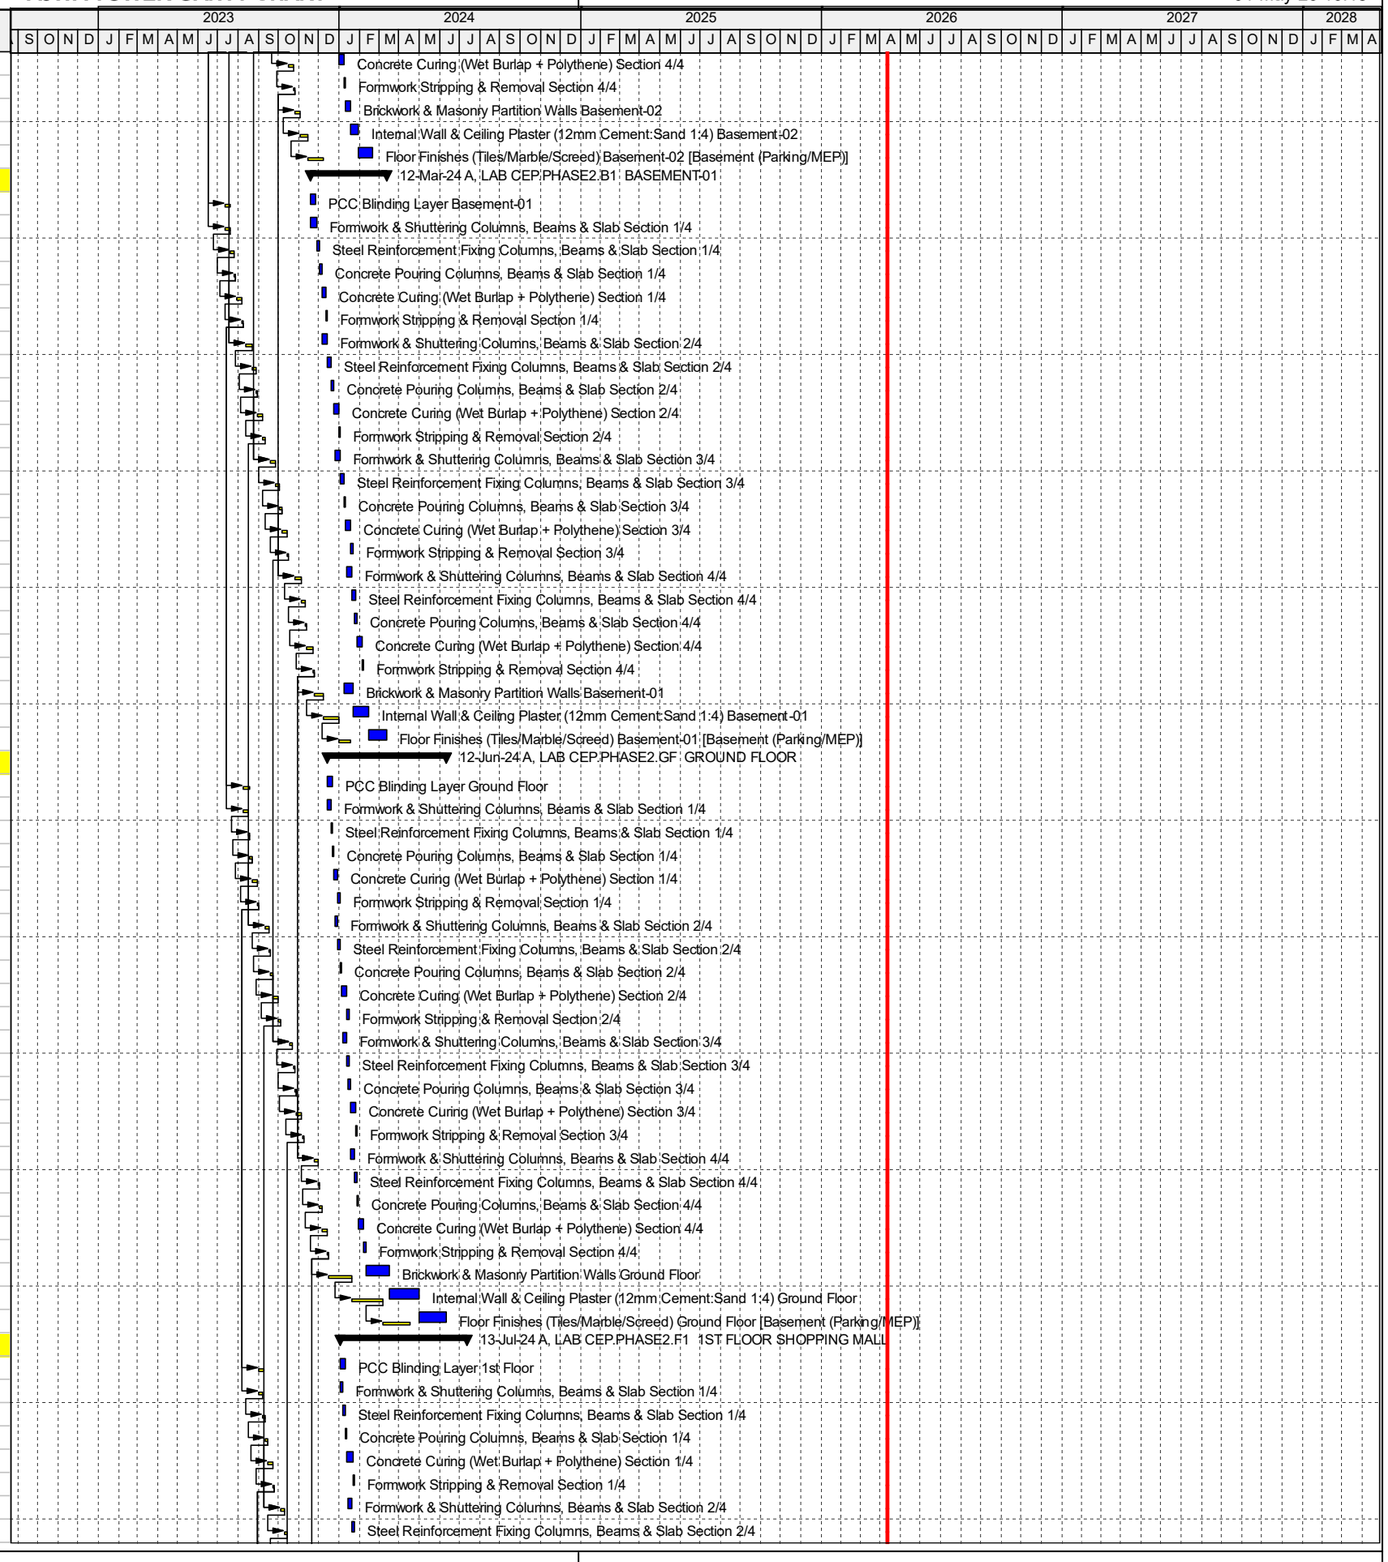




© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A2770 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 24-Jan-24 A | 27-Jan-24 A | 13-Oct-23 | 16-Oct-23 |
| A2780 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 27-Jan-24 A | 05-Feb-24 A | 17-Oct-23 | 24-Oct-23 |
| A2790 | Formwork Stripping & Removal Section 2/4 | 3 | 05-Feb-24 A | 07-Feb-24 A | 25-Oct-23 | 27-Oct-23 |
| A2800 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 5 | 29-Jan-24 A | 03-Feb-24 A | 08-Nov-23 | 14-Nov-23 |
| A2810 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 4 | 03-Feb-24 A | 08-Feb-24 A | 14-Nov-23 | 18-Nov-23 |
| A2820 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 08-Feb-24 A | 10-Feb-24 A | 18-Nov-23 | 21-Nov-23 |
| A2830 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 10-Feb-24 A | 17-Feb-24 A | 21-Nov-23 | 29-Nov-23 |
| A2840 | Formwork Stripping & Removal Section 3/4 | 3 | 17-Feb-24 A | 01-Mar-24 A | 29-Nov-23 | 02-Dec-23 |
| A2850 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 5 | 12-Feb-24 A | 17-Feb-24 A | 16-Dec-23 | 22-Dec-23 |
| A2860 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 4 | 17-Feb-24 A | 02-Mar-24 A | 22-Dec-23 | 27-Dec-23 |
| A2870 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 02-Mar-24 A | 05-Mar-24 A | 27-Dec-23 | 29-Dec-23 |
| A2880 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 05-Mar-24 A | 13-Mar-24 A | 30-Dec-23 | 06-Jan-24 |
| A2890 | Formwork Stripping & Removal Section 4/4 | 3 | 13-Mar-24 A | 15-Mar-24 A | 08-Jan-24 | 10-Jan-24 |
| A2900 | Brickwork & Masonry Partition Walls 1st Floor | 30 | 15-Mar-24 A | 18-Apr-24 A | 10-Jan-24 | 14-Feb-24 |
| A2910 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 1st Fl | 40 | 18-Apr-24 A | 03-Jun-24 A | 14-Feb-24 | 01-Apr-24 |
| A2920 | Floor Finishes (Tiles/Marble/Screed) 1st Floor [Basement (Parki | 35 | 03-Jun-24 A | 13-Jul-24 A | 01-Apr-24 | 11-May-24 |
| **LAB CEP.PHASE2.2F 2ND FLOOR SHOPPING MALL** | | 170 | 24-Jan-24 A | 08-Aug-24 A | 25-Sep-23 | 05-Jun-24 |
| A2930 | PCC Blinding Layer 2nd Floor | 8 | 24-Jan-24 A | 01-Feb-24 A | 25-Sep-23 | 04-Oct-23 |
| A2940 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 24-Jan-24 A | 29-Jan-24 A | 25-Sep-23 | 30-Sep-23 |
| A2950 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 4 | 29-Jan-24 A | 01-Feb-24 A | 30-Sep-23 | 05-Oct-23 |
| A2960 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 01-Feb-24 A | 05-Feb-24 A | 05-Oct-23 | 07-Oct-23 |
| A2970 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 05-Feb-24 A | 13-Feb-24 A | 09-Oct-23 | 16-Oct-23 |
| A2980 | Formwork Stripping & Removal Section 1/4 | 3 | 13-Feb-24 A | 15-Feb-24 A | 17-Oct-23 | 19-Oct-23 |
| A2990 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 5 | 06-Feb-24 A | 12-Feb-24 A | 27-Oct-23 | 02-Nov-23 |
| A3000 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 4 | 12-Feb-24 A | 15-Feb-24 A | 02-Nov-23 | 07-Nov-23 |
| A3010 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 28-Feb-24 A | 02-Mar-24 A | 07-Nov-23 | 09-Nov-23 |
| A3020 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 02-Mar-24 A | 09-Mar-24 A | 09-Nov-23 | 17-Nov-23 |
| A3030 | Formwork Stripping & Removal Section 2/4 | 3 | 09-Mar-24 A | 12-Mar-24 A | 17-Nov-23 | 21-Nov-23 |
| A3040 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 5 | 04-Mar-24 A | 09-Mar-24 A | 02-Dec-23 | 08-Dec-23 |
| A3050 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 4 | 09-Mar-24 A | 13-Mar-24 A | 08-Dec-23 | 12-Dec-23 |
| A3060 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 13-Mar-24 A | 15-Mar-24 A | 13-Dec-23 | 15-Dec-23 |
| A3070 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 15-Mar-24 A | 23-Mar-24 A | 15-Dec-23 | 23-Dec-23 |
| A3080 | Formwork Stripping & Removal Section 3/4 | 3 | 23-Mar-24 A | 26-Mar-24 A | 23-Dec-23 | 26-Dec-23 |
| A3090 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 5 | 16-Mar-24 A | 22-Mar-24 A | 10-Jan-24 | 16-Jan-24 |
| A3100 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 4 | 22-Mar-24 A | 27-Mar-24 A | 16-Jan-24 | 20-Jan-24 |
| A3110 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 27-Mar-24 A | 29-Mar-24 A | 20-Jan-24 | 23-Jan-24 |
| A3120 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 29-Mar-24 A | 05-Apr-24 A | 23-Jan-24 | 31-Jan-24 |
| A3130 | Formwork Stripping & Removal Section 4/4 | 3 | 05-Apr-24 A | 08-Apr-24 A | 31-Jan-24 | 03-Feb-24 |
| A3140 | Brickwork & Masonry Partition Walls 2nd Floor | 30 | 08-Apr-24 A | 13-May-24 A | 03-Feb-24 | 09-Mar-24 |
| A3150 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 2nd F | 40 | 13-May-24 A | 28-Jun-24 A | 09-Mar-24 | 25-Apr-24 |
| A3160 | Floor Finishes (Tiles/Marble/Screed) 2nd Floor [Basement (Park | 35 | 28-Jun-24 A | 08-Aug-24 A | 25-Apr-24 | 05-Jun-24 |
| **LAB CEP.PHASE2.3F 3RD FLOOR SHOPPING MALL** | | 164 | 15-Feb-24 A | 24-Aug-24 A | 19-Oct-23 | 01-Jul-24 |
| A3170 | PCC Blinding Layer 3rd Floor | 8 | 15-Feb-24 A | 23-Feb-24 A | 19-Oct-23 | 27-Oct-23 |
| A3180 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 15-Feb-24 A | 20-Feb-24 A | 19-Oct-23 | 25-Oct-23 |
| A3190 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 4 | 20-Feb-24 A | 23-Feb-24 A | 25-Oct-23 | 30-Oct-23 |
| A3200 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 23-Feb-24 A | 27-Feb-24 A | 30-Oct-23 | 01-Nov-23 |
| A3210 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 27-Feb-24 A | 06-Mar-24 A | 01-Nov-23 | 09-Nov-23 |
| A3220 | Formwork Stripping & Removal Section 1/4 | 3 | 06-Mar-24 A | 08-Mar-24 A | 09-Nov-23 | 13-Nov-23 |
| A3230 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 28-Feb-24 A | 06-Mar-24 A | 21-Nov-23 | 28-Nov-23 |
| A3240 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 4 | 06-Mar-24 A | 11-Mar-24 A | 28-Nov-23 | 02-Dec-23 |
| A3250 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 11-Mar-24 A | 13-Mar-24 A | 02-Dec-23 | 05-Dec-23 |
| A3260 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 13-Mar-24 A | 20-Mar-24 A | 05-Dec-23 | 13-Dec-23 |
| A3270 | Formwork Stripping & Removal Section 2/4 | 3 | 20-Mar-24 A | 22-Mar-24 A | 13-Dec-23 | 16-Dec-23 |
| A3280 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 14-Mar-24 A | 21-Mar-24 A | 27-Dec-23 | 03-Jan-24 |
| A3290 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 4 | 21-Mar-24 A | 26-Mar-24 A | 03-Jan-24 | 06-Jan-24 |
| A3300 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 26-Mar-24 A | 28-Mar-24 A | 08-Jan-24 | 10-Jan-24 |
| A3310 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 28-Mar-24 A | 05-Apr-24 A | 10-Jan-24 | 18-Jan-24 |
| A3320 | Formwork Stripping & Removal Section 3/4 | 3 | 05-Apr-24 A | 09-Apr-24 A | 18-Jan-24 | 20-Jan-24 |
| A3330 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 29-Mar-24 A | 05-Apr-24 A | 03-Feb-24 | 10-Feb-24 |
| A3340 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 4 | 05-Apr-24 A | 10-Apr-24 A | 10-Feb-24 | 15-Feb-24 |
| A3350 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 10-Apr-24 A | 12-Apr-24 A | 15-Feb-24 | 17-Feb-24 |
| A3360 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 12-Apr-24 A | 20-Apr-24 A | 17-Feb-24 | 26-Feb-24 |
| A3370 | Formwork Stripping & Removal Section 4/4 | 3 | 20-Apr-24 A | 24-Apr-24 A | 26-Feb-24 | 29-Feb-24 |
| A3380 | Brickwork & Masonry Partition Walls 3rd Floor | 30 | 24-Apr-24 A | 29-May-24 A | 29-Feb-24 | 04-Apr-24 |

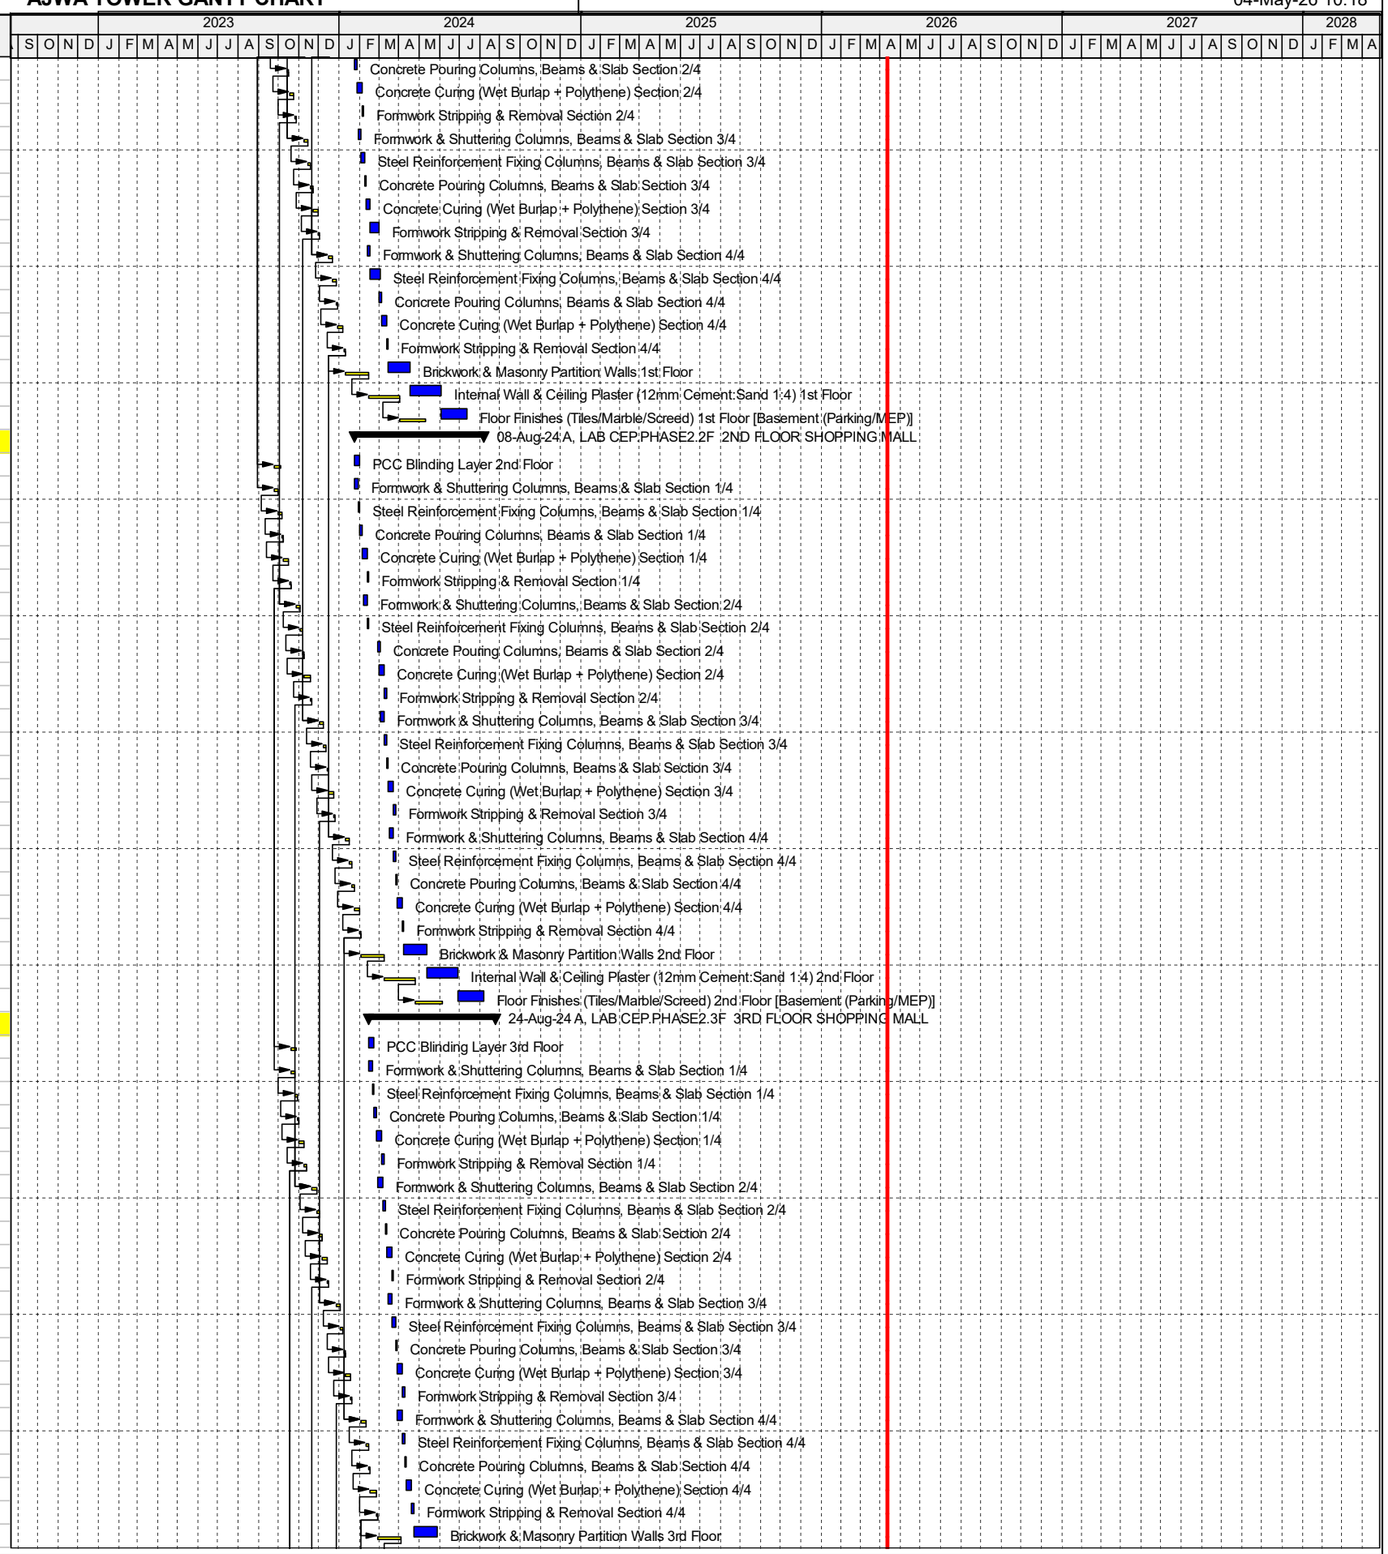


Actual Level of Effort | Actual Work | Critical Remaining Work


Primary Baseline | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation


| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A3390 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 3rd F | 40 | 29-May-24 A | 15-Jul-24 A | 04-Apr-24 | 21-May-24 |
| A3400 | Floor Finishes (Tiles/Marble/Screed) 3rd Floor [Basement (Parki | 35 | 15-Jul-24 A | 24-Aug-24 A | 21-May-24 | 01-Jul-24 |
| **LAB CEP.PHASE2.4F 4TH FLOOR FOOD COURT** | | 127 | 08-Mar-24 A | 02-Aug-24 A | 13-Nov-23 | 23-Jul-24 |
| A3410 | PCC Blinding Layer 4th Floor | 8 | 08-Mar-24 A | 16-Mar-24 A | 13-Nov-23 | 21-Nov-23 |
| A3420 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 08-Mar-24 A | 15-Mar-24 A | 13-Nov-23 | 20-Nov-23 |
| A3430 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 15-Mar-24 A | 18-Mar-24 A | 20-Nov-23 | 22-Nov-23 |
| A3440 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 18-Mar-24 A | 19-Mar-24 A | 23-Nov-23 | 24-Nov-23 |
| A3450 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 19-Mar-24 A | 26-Mar-24 A | 24-Nov-23 | 02-Dec-23 |
| A3460 | Formwork Stripping & Removal Section 1/4 | 3 | 26-Mar-24 A | 28-Mar-24 A | 02-Dec-23 | 05-Dec-23 |
| A3470 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 7 | 20-Mar-24 A | 28-Mar-24 A | 16-Dec-23 | 25-Dec-23 |
| A3480 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 28-Mar-24 A | 30-Mar-24 A | 25-Dec-23 | 27-Dec-23 |
| A3490 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 30-Mar-24 A | 01-Apr-24 A | 27-Dec-23 | 28-Dec-23 |
| A3500 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 01-Apr-24 A | 08-Apr-24 A | 29-Dec-23 | 05-Jan-24 |
| A3510 | Formwork Stripping & Removal Section 2/4 | 3 | 08-Apr-24 A | 10-Apr-24 A | 06-Jan-24 | 09-Jan-24 |
| A3520 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 02-Apr-24 A | 09-Apr-24 A | 22-Jan-24 | 29-Jan-24 |
| A3530 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 09-Apr-24 A | 11-Apr-24 A | 29-Jan-24 | 31-Jan-24 |
| A3540 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 11-Apr-24 A | 12-Apr-24 A | 31-Jan-24 | 01-Feb-24 |
| A3550 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 12-Apr-24 A | 20-Apr-24 A | 02-Feb-24 | 09-Feb-24 |
| A3560 | Formwork Stripping & Removal Section 3/4 | 7 | 20-Apr-24 A | 29-Apr-24 A | 10-Feb-24 | 17-Feb-24 |
| A3570 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 13-Apr-24 A | 20-Apr-24 A | 29-Feb-24 | 07-Mar-24 |
| A3580 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 20-Apr-24 A | 24-Apr-24 A | 07-Mar-24 | 09-Mar-24 |
| A3590 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 24-Apr-24 A | 25-Apr-24 A | 11-Mar-24 | 12-Mar-24 |
| A3600 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 25-Apr-24 A | 03-May-24 A | 12-Mar-24 | 20-Mar-24 |
| A3610 | Formwork Stripping & Removal Section 4/4 | 3 | 03-May-24 A | 06-May-24 A | 20-Mar-24 | 22-Mar-24 |
| A3620 | Brickwork & Masonry Partition Walls 4th Floor | 30 | 06-May-24 A | 08-Jun-24 A | 22-Mar-24 | 26-Apr-24 |
| A3630 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 4th F | 40 | 08-Jun-24 A | 24-Jul-24 A | 26-Apr-24 | 12-Jun-24 |
| A3640 | Floor Finishes (Tiles/Marble/Screed) 4th Floor [Basement (Parki | 35 | 24-Jun-24 A | 02-Aug-24 A | 12-Jun-24 | 23-Jul-24 |
| **LAB CEP.PHASE2.5F 5TH FLOOR FOOD COURT** | | 155 | 28-Mar-24 A | 25-Sep-24 A | 05-Dec-23 | 15-Aug-24 |
| A3650 | PCC Blinding Layer 5th Floor | 8 | 28-Mar-24 A | 05-Apr-24 A | 05-Dec-23 | 14-Dec-23 |
| A3660 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 28-Mar-24 A | 04-Apr-24 A | 05-Dec-23 | 12-Dec-23 |
| A3670 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 04-Apr-24 A | 06-Apr-24 A | 13-Dec-23 | 15-Dec-23 |
| A3680 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 06-Apr-24 A | 08-Apr-24 A | 15-Dec-23 | 16-Dec-23 |
| A3690 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 08-Apr-24 A | 15-Apr-24 A | 16-Dec-23 | 25-Dec-23 |
| A3700 | Formwork Stripping & Removal Section 1/4 | 3 | 15-Apr-24 A | 17-Apr-24 A | 25-Dec-23 | 28-Dec-23 |
| A3710 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 09-Apr-24 A | 16-Apr-24 A | 09-Jan-24 | 16-Jan-24 |
| A3720 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 16-Apr-24 A | 18-Apr-24 A | 16-Jan-24 | 19-Jan-24 |
| A3730 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 18-Apr-24 A | 19-Apr-24 A | 19-Jan-24 | 20-Jan-24 |
| A3740 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 19-Apr-24 A | 27-Apr-24 A | 20-Jan-24 | 29-Jan-24 |
| A3750 | Formwork Stripping & Removal Section 2/4 | 3 | 27-Apr-24 A | 30-Apr-24 A | 29-Jan-24 | 31-Jan-24 |
| A3760 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 20-Apr-24 A | 27-Apr-24 A | 19-Feb-24 | 26-Feb-24 |
| A3770 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 27-Apr-24 A | 01-May-24 A | 26-Feb-24 | 28-Feb-24 |
| A3780 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 01-May-24 A | 02-May-24 A | 28-Feb-24 | 29-Feb-24 |
| A3790 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 02-May-24 A | 10-May-24 A | 01-Mar-24 | 08-Mar-24 |
| A3800 | Formwork Stripping & Removal Section 3/4 | 3 | 10-May-24 A | 13-May-24 A | 09-Mar-24 | 12-Mar-24 |
| A3810 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 03-May-24 A | 10-May-24 A | 22-Mar-24 | 29-Mar-24 |
| A3820 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 10-May-24 A | 13-May-24 A | 30-Mar-24 | 02-Apr-24 |
| A3830 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 13-May-24 A | 14-May-24 A | 02-Apr-24 | 03-Apr-24 |
| A3840 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 14-May-24 A | 22-May-24 A | 03-Apr-24 | 11-Apr-24 |
| A3850 | Formwork Stripping & Removal Section 4/4 | 3 | 22-May-24 A | 25-May-24 A | 11-Apr-24 | 15-Apr-24 |
| A3860 | Brickwork & Masonry Partition Walls 5th Floor | 30 | 25-May-24 A | 29-Jun-24 A | 15-Apr-24 | 20-May-24 |
| A3870 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 5th F | 40 | 29-Jun-24 A | 15-Aug-24 A | 20-May-24 | 05-Jul-24 |
| A3880 | Floor Finishes (Tiles/Marble/Screed) 5th Floor [Basement (Parki | 35 | 15-Aug-24 A | 25-Sep-24 A | 05-Jul-24 | 15-Aug-24 |
| **LAB CEP.PHASE2.6F 6TH FLOOR FOOD COURT & ENTERTAINM** | | 156 | 17-Apr-24 A | 16-Oct-24 A | 28-Dec-23 | 06-Sep-24 |
| A3890 | PCC Blinding Layer 6th Floor | 8 | 17-Apr-24 A | 25-Apr-24 A | 28-Dec-23 | 06-Jan-24 |
| A3900 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 17-Apr-24 A | 24-Apr-24 A | 28-Dec-23 | 04-Jan-24 |
| A3910 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 24-Apr-24 A | 26-Apr-24 A | 04-Jan-24 | 06-Jan-24 |
| A3920 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 26-Apr-24 A | 27-Apr-24 A | 08-Jan-24 | 09-Jan-24 |
| A3930 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 27-Apr-24 A | 04-May-24 A | 09-Jan-24 | 17-Jan-24 |
| A3940 | Formwork Stripping & Removal Section 1/4 | 3 | 04-May-24 A | 07-May-24 A | 17-Jan-24 | 19-Jan-24 |
| A1100 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 29-Apr-24 A | 06-May-24 A | 01-Feb-24 | 08-Feb-24 |
| A3960 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 06-May-24 A | 08-May-24 A | 08-Feb-24 | 10-Feb-24 |
| A3970 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 08-May-24 A | 09-May-24 A | 10-Feb-24 | 12-Feb-24 |
| A3980 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 09-May-24 A | 17-May-24 A | 13-Feb-24 | 20-Feb-24 |
| A3990 | Formwork Stripping & Removal Section 2/4 | 3 | 17-May-24 A | 20-May-24 A | 21-Feb-24 | 23-Feb-24 |

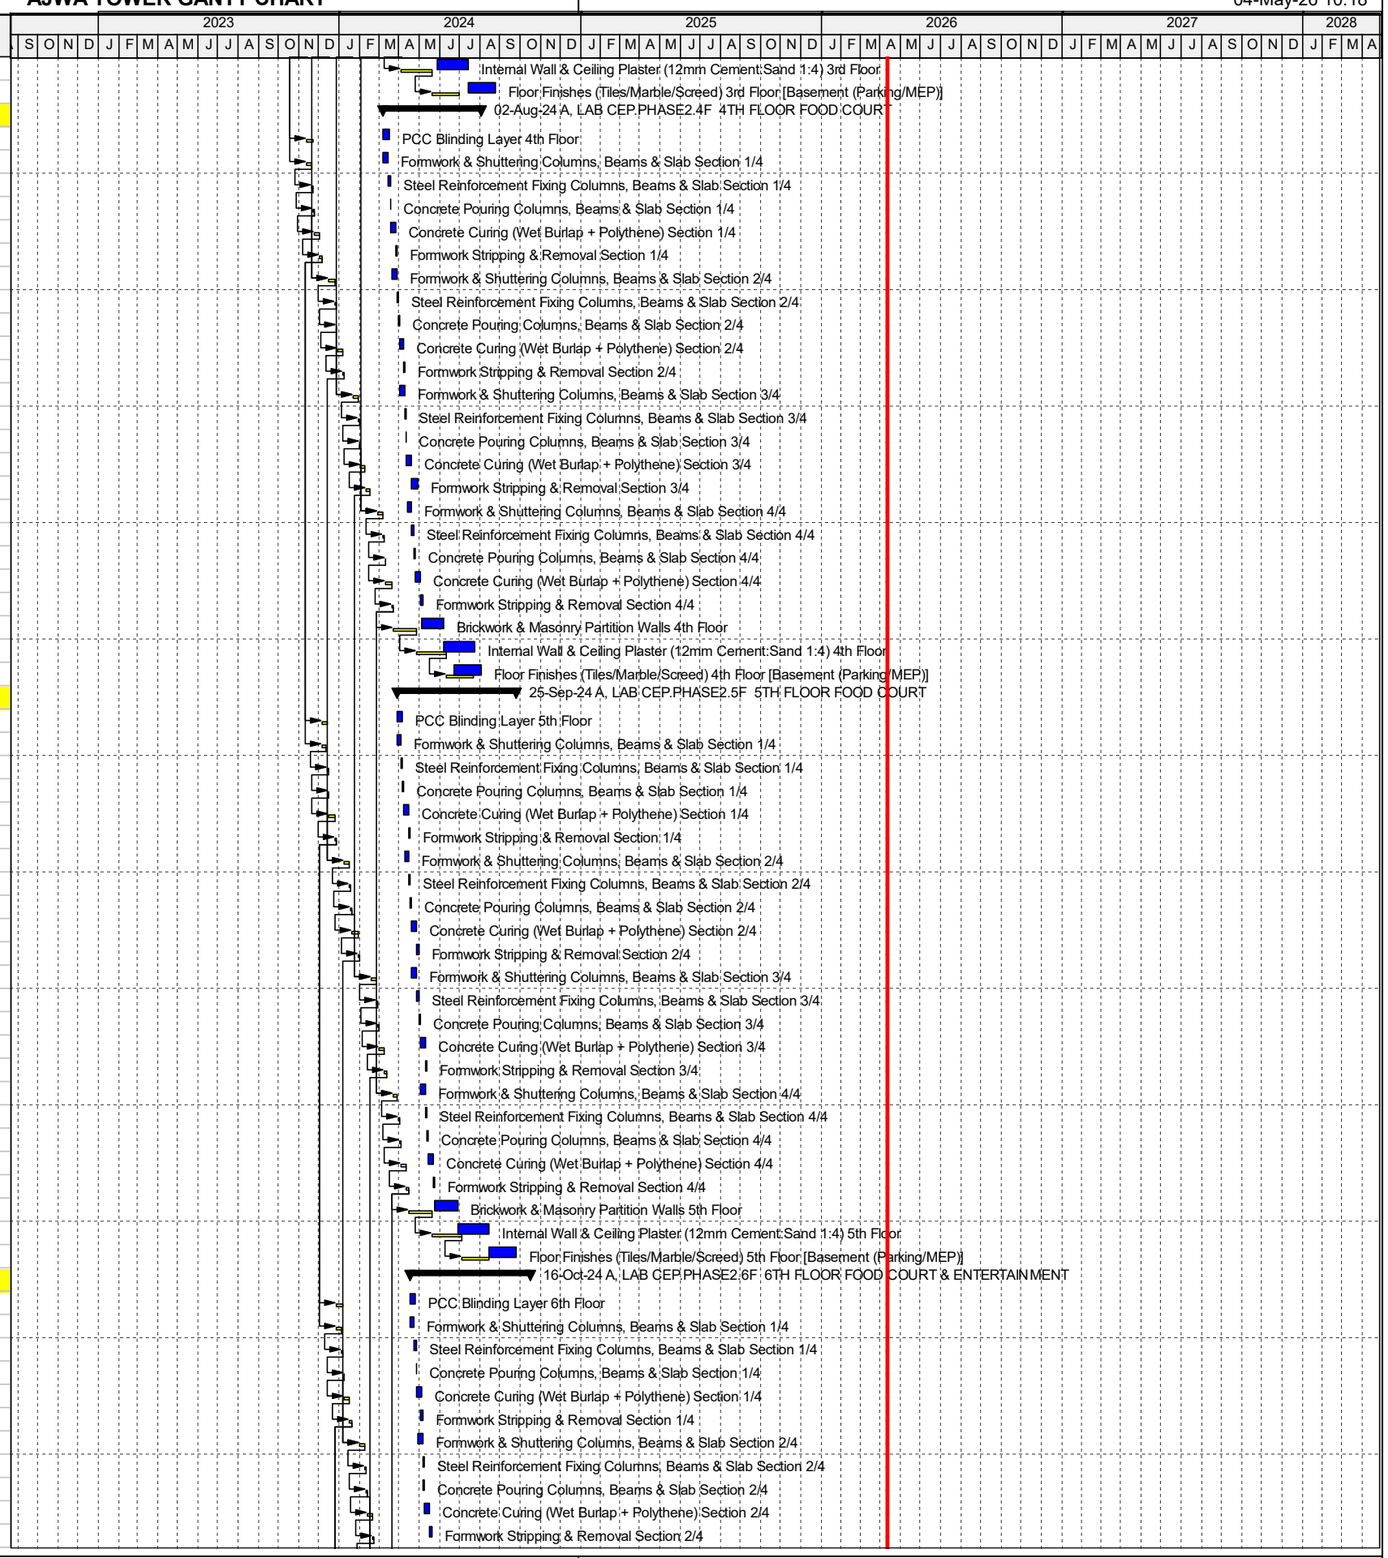




© Oracle Corporation


| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A4000 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 10-May-24 A | 17-May-24 A | 12-Mar-24 | 19-Mar-24 |
| A4010 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 17-May-24 A | 21-May-24 A | 19-Mar-24 | 22-Mar-24 |
| A4020 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 21-May-24 A | 22-May-24 A | 22-Mar-24 | 23-Mar-24 |
| A4030 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 22-May-24 A | 30-May-24 A | 23-Mar-24 | 01-Apr-24 |
| A4040 | Formwork Stripping & Removal Section 3/4 | 3 | 30-May-24 A | 01-Jun-24 A | 01-Apr-24 | 03-Apr-24 |
| A4050 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 23-May-24 A | 30-May-24 A | 15-Apr-24 | 22-Apr-24 |
| A4060 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 30-May-24 A | 03-Jun-24 A | 22-Apr-24 | 24-Apr-24 |
| A4070 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 03-Jun-24 A | 04-Jun-24 A | 25-Apr-24 | 26-Apr-24 |
| A4080 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 04-Jun-24 A | 12-Jun-24 A | 26-Apr-24 | 04-May-24 |
| A4090 | Formwork Stripping & Removal Section 4/4 | 3 | 12-Jun-24 A | 15-Jun-24 A | 04-May-24 | 07-May-24 |
| A4100 | Brickwork & Masonry Partition Walls 6th Floor | 30 | 15-Jun-24 A | 20-Jul-24 A | 07-May-24 | 11-Jun-24 |
| A4110 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 6th F | 40 | 20-Jul-24 A | 05-Sep-24 A | 11-Jun-24 | 27-Jul-24 |
| A4120 | Floor Finishes (Tiles/Marble/Screed) 6th Floor [Basement (Parki | 35 | 05-Sep-24 A | 16-Oct-24 A | 27-Jul-24 | 06-Sep-24 |
| LAB CEP.PHASE2.SF | SERVICE FLOOR MEP SERVICES FLOOR | 122 | 07-May-24 A | 25-Sep-24 A | 19-Jan-24 | 12-Aug-24 |
| A4130 | PCC Blinding Layer Service Floor | 8 | 07-May-24 A | 15-May-24 A | 19-Jan-24 | 29-Jan-24 |
| A4140 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 07-May-24 A | 14-May-24 A | 19-Jan-24 | 26-Jan-24 |
| A4150 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 5 | 14-May-24 A | 20-May-24 A | 27-Jan-24 | 01-Feb-24 |
| A4160 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 3 | 20-May-24 A | 22-May-24 A | 02-Feb-24 | 05-Feb-24 |
| A4170 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 22-May-24 A | 30-May-24 A | 05-Feb-24 | 13-Feb-24 |
| A4180 | Formwork Stripping & Removal Section 1/4 | 3 | 30-May-24 A | 03-Jun-24 A | 13-Feb-24 | 15-Feb-24 |
| A4190 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 23-May-24 A | 30-May-24 A | 23-Feb-24 | 01-Mar-24 |
| A4200 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 5 | 30-May-24 A | 05-Jun-24 A | 01-Mar-24 | 07-Mar-24 |
| A4210 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 3 | 05-Jun-24 A | 07-Jun-24 A | 07-Mar-24 | 11-Mar-24 |
| A4220 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 07-Jun-24 A | 14-Jun-24 A | 11-Mar-24 | 19-Mar-24 |
| A4230 | Formwork Stripping & Removal Section 2/4 | 3 | 14-Jun-24 A | 18-Jun-24 A | 19-Mar-24 | 21-Mar-24 |
| A4240 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 08-Jun-24 A | 15-Jun-24 A | 04-Apr-24 | 11-Apr-24 |
| A4250 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 5 | 15-Jun-24 A | 21-Jun-24 A | 11-Apr-24 | 17-Apr-24 |
| A4260 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 3 | 21-Jun-24 A | 24-Jun-24 A | 17-Apr-24 | 19-Apr-24 |
| A4270 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 24-Jun-24 A | 01-Jul-24 A | 19-Apr-24 | 27-Apr-24 |
| A4280 | Formwork Stripping & Removal Section 3/4 | 3 | 02-Jul-24 A | 04-Jul-24 A | 27-Apr-24 | 01-May-24 |
| A4290 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 25-Jun-24 A | 25-Jul-24 A | 07-May-24 | 14-May-24 |
| A4300 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 5 | 25-Jul-24 A | 30-Jul-24 A | 15-May-24 | 20-May-24 |
| A4310 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 3 | 30-Jul-24 A | 01-Aug-24 A | 21-May-24 | 23-May-24 |
| A4320 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 01-Aug-24 A | 09-Aug-24 A | 23-May-24 | 31-May-24 |
| A4330 | Formwork Stripping & Removal Section 4/4 | 3 | 09-Aug-24 A | 12-Aug-24 A | 31-May-24 | 03-Jun-24 |
| A4340 | Brickwork & Masonry Partition Walls Service Floor | 15 | 12-Aug-24 A | 28-Aug-24 A | 04-Jun-24 | 20-Jun-24 |
| A4350 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) Servi | 25 | 28-Aug-24 A | 25-Sep-24 A | 21-Jun-24 | 19-Jul-24 |
| A4360 | Floor Finishes (Tiles/Marble/Screed) Service Floor [Basement (F | 20 | 03-Jun-24 A | 25-Jun-24 A | 20-Jul-24 | 12-Aug-24 |
| LAB CEP.PHASE2.7F | 7TH FLOOR OFFICE FLOOR | 250 | 03-Jun-24 A | 20-Mar-25 A | 16-Feb-24 | 30-Nov-24 |
| A4370 | PCC Blinding Layer 7th Floor | 8 | 03-Jun-24 A | 11-Jun-24 A | 16-Feb-24 | 24-Feb-24 |
| A4380 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 03-Jun-24 A | 10-Jun-24 A | 16-Feb-24 | 23-Feb-24 |
| A4390 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 10-Jun-24 A | 12-Jun-24 A | 23-Feb-24 | 26-Feb-24 |
| A4400 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 12-Jun-24 A | 13-Jun-24 A | 26-Feb-24 | 27-Feb-24 |
| A4410 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 13-Jun-24 A | 20-Jun-24 A | 28-Feb-24 | 06-Mar-24 |
| A4420 | Formwork Stripping & Removal Section 1/4 | 3 | 20-Jun-24 A | 22-Jun-24 A | 07-Mar-24 | 09-Mar-24 |
| A4430 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 14-Jun-24 A | 21-Jun-24 A | 21-Mar-24 | 28-Mar-24 |
| A4440 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 21-Jun-24 A | 24-Jun-24 A | 29-Mar-24 | 01-Apr-24 |
| A4450 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 26-Jul-24 A | 27-Jul-24 A | 01-Apr-24 | 02-Apr-24 |
| A4460 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 27-Jul-24 A | 05-Aug-24 A | 02-Apr-24 | 10-Apr-24 |
| A4470 | Formwork Stripping & Removal Section 2/4 | 3 | 05-Aug-24 A | 07-Aug-24 A | 10-Apr-24 | 13-Apr-24 |
| A4480 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 29-Jul-24 A | 05-Aug-24 A | 01-May-24 | 08-May-24 |
| A4490 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 05-Aug-24 A | 07-Aug-24 A | 08-May-24 | 10-May-24 |
| A4500 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 07-Aug-24 A | 08-Aug-24 A | 11-May-24 | 13-May-24 |
| A4510 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 08-Aug-24 A | 16-Aug-24 A | 13-May-24 | 21-May-24 |
| A4520 | Formwork Stripping & Removal Section 3/4 | 3 | 16-Aug-24 A | 19-Aug-24 A | 21-May-24 | 23-May-24 |
| A4530 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 09-Aug-24 A | 16-Aug-24 A | 04-Jun-24 | 11-Jun-24 |
| A1100 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 16-Aug-24 A | 20-Aug-24 A | 11-Jun-24 | 13-Jun-24 |
| A4550 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 20-Aug-24 A | 21-Aug-24 A | 13-Jun-24 | 14-Jun-24 |
| A4560 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 21-Aug-24 A | 29-Aug-24 A | 15-Jun-24 | 22-Jun-24 |
| A4570 | Formwork Stripping & Removal Section 4/4 | 3 | 29-Aug-24 A | 31-Aug-24 A | 24-Jun-24 | 26-Jun-24 |
| A4580 | Brickwork & Masonry Partition Walls 7th Floor | 40 | 16-Oct-24 A | 30-Nov-24 A | 26-Jun-24 | 12-Aug-24 |
| A4590 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 7th F | 50 | 02-Dec-24 A | 28-Jan-25 A | 12-Aug-24 | 09-Oct-24 |
| A4600 | Floor Finishes (Tiles/Marble/Screed) 7th Floor [Basement (Parki | 45 | 28-Jan-25 A | 20-Mar-25 A | 09-Oct-24 | 30-Nov-24 |
| LAB CEP.PHASE2.8F | 8TH FLOOR LOBBY | 210 | 22-Jun-24 A | 22-Feb-25 A | 09-Mar-24 | 23-Dec-24 |

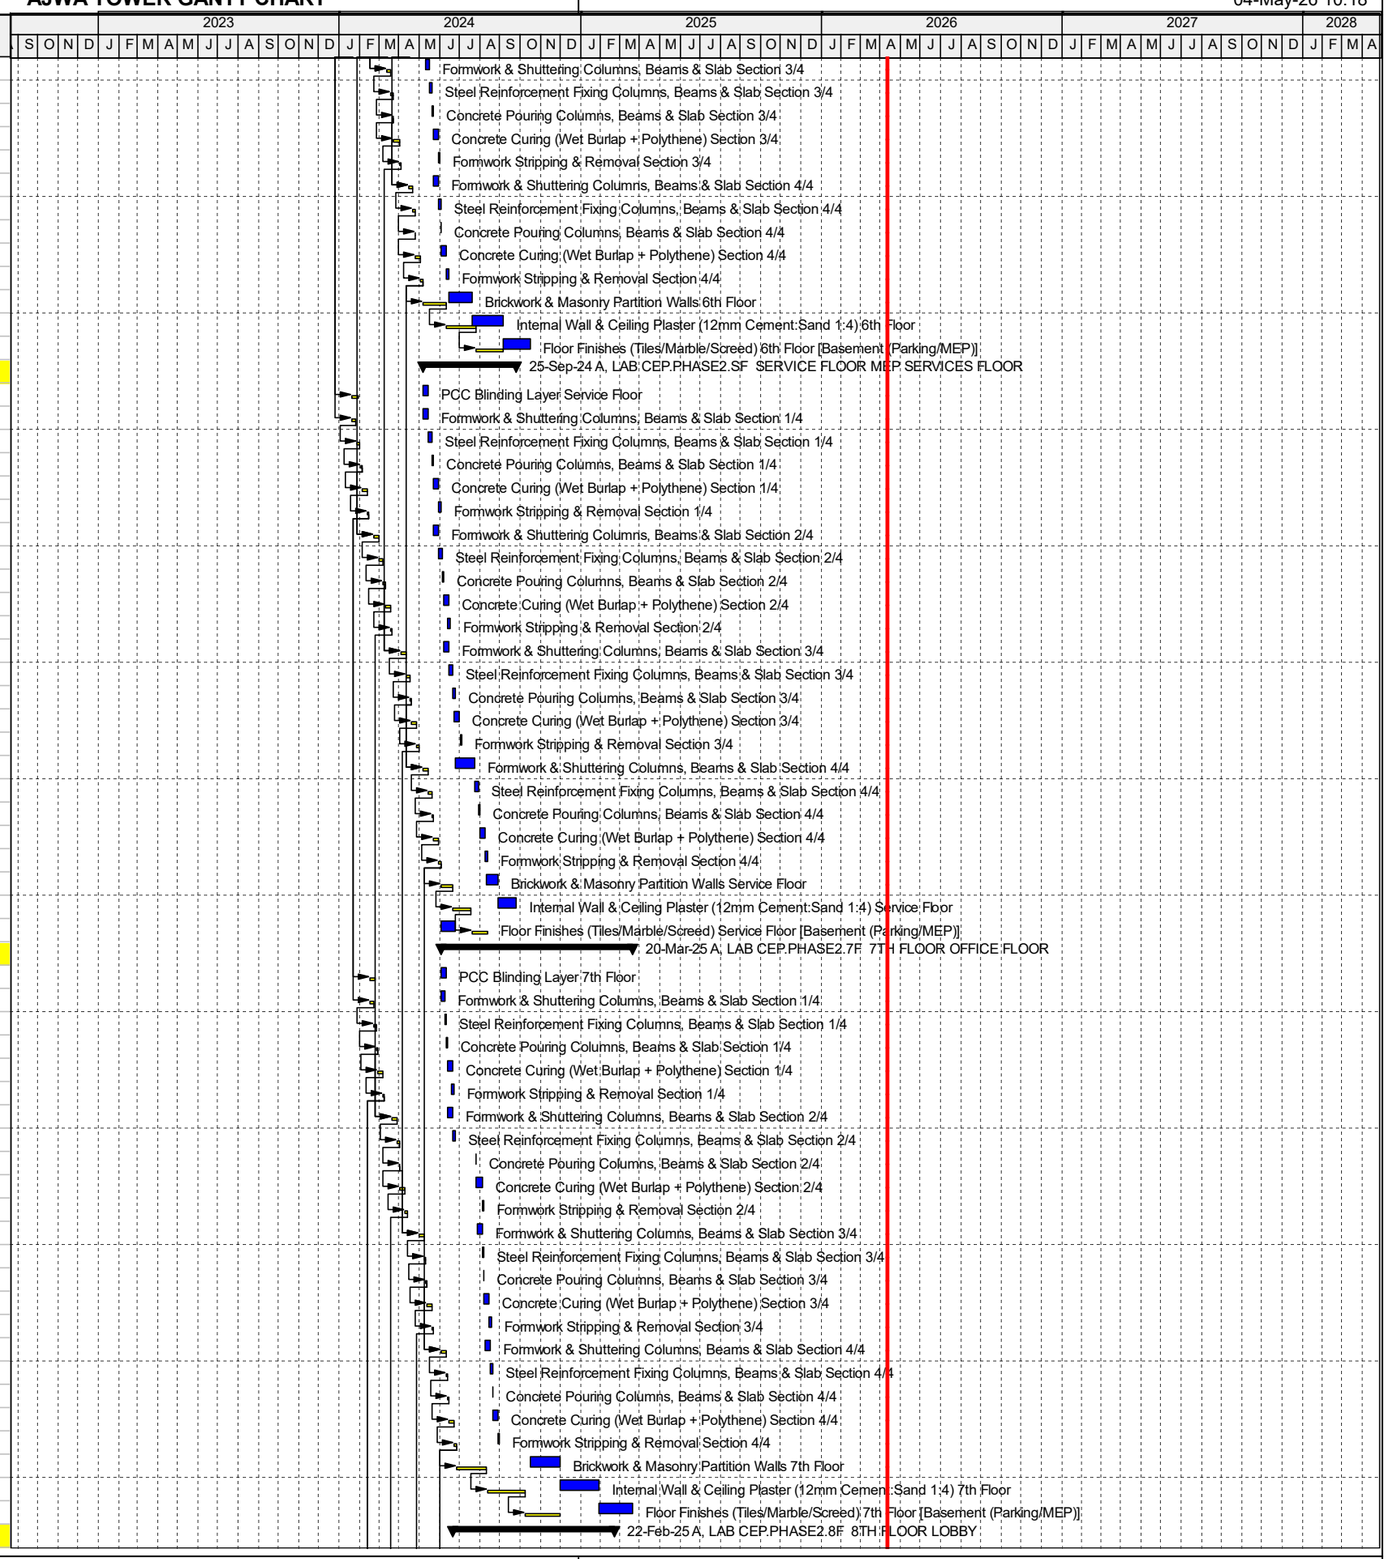




© Oracle Corporation


| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A4610 | PCC Blinding Layer 8th Floor | 8 | 22-Jun-24 A | 30-Jul-24 A | 09-Mar-24 | 18-Mar-24 |
| A4620 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 22-Jun-24 A | 29-Jul-24 A | 09-Mar-24 | 16-Mar-24 |
| A4630 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 29-Jul-24 A | 31-Jul-24 A | 16-Mar-24 | 20-Mar-24 |
| A4640 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 31-Jul-24 A | 01-Aug-24 A | 20-Mar-24 | 21-Mar-24 |
| A4650 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 01-Aug-24 A | 09-Aug-24 A | 21-Mar-24 | 29-Mar-24 |
| A4660 | Formwork Stripping & Removal Section 1/4 | 3 | 09-Aug-24 A | 13-Aug-24 A | 29-Mar-24 | 01-Apr-24 |
| A4670 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 02-Aug-24 A | 09-Aug-24 A | 13-Apr-24 | 20-Apr-24 |
| A4680 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 09-Aug-24 A | 12-Aug-24 A | 20-Apr-24 | 23-Apr-24 |
| A4690 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 12-Aug-24 A | 13-Aug-24 A | 24-Apr-24 | 25-Apr-24 |
| A4700 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 13-Aug-24 A | 21-Aug-24 A | 25-Apr-24 | 03-May-24 |
| A4710 | Formwork Stripping & Removal Section 2/4 | 3 | 21-Aug-24 A | 23-Aug-24 A | 03-May-24 | 06-May-24 |
| A4720 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 14-Aug-24 A | 21-Aug-24 A | 23-May-24 | 30-May-24 |
| A4730 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 21-Aug-24 A | 24-Aug-24 A | 31-May-24 | 03-Jun-24 |
| A4740 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 24-Aug-24 A | 26-Aug-24 A | 03-Jun-24 | 04-Jun-24 |
| A4750 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 26-Aug-24 A | 03-Sep-24 A | 04-Jun-24 | 12-Jun-24 |
| A4760 | Formwork Stripping & Removal Section 3/4 | 3 | 03-Sep-24 A | 05-Sep-24 A | 12-Jun-24 | 15-Jun-24 |
| A4770 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 27-Aug-24 A | 03-Sep-24 A | 26-Jun-24 | 03-Jul-24 |
| A4780 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 03-Sep-24 A | 05-Sep-24 A | 03-Jul-24 | 06-Jul-24 |
| A4790 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 05-Sep-24 A | 06-Sep-24 A | 06-Jul-24 | 08-Jul-24 |
| A4800 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 06-Sep-24 A | 14-Sep-24 A | 08-Jul-24 | 16-Jul-24 |
| A4810 | Formwork Stripping & Removal Section 4/4 | 3 | 14-Sep-24 A | 18-Sep-24 A | 16-Jul-24 | 18-Jul-24 |
| A4820 | Brickwork & Masonry Partition Walls 8th Floor | 40 | 18-Sep-24 A | 04-Nov-24 A | 19-Jul-24 | 03-Sep-24 |
| A4830 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 8th F | 50 | 04-Nov-24 A | 01-Jan-25 A | 04-Sep-24 | 31-Oct-24 |
| A4840 | Floor Finishes (Tiles/Marble/Screed) 8th Floor [Basement (Parki | 45 | 01-Jan-25 A | 22-Feb-25 A | 01-Nov-24 | 23-Dec-24 |
| LAB CEP.PHASE2.9F 9TH FLOOR RESIDENTIAL APPARTMENTS | | 167 | 03-Aug-24 A | 13-Feb-25 A | 02-Apr-24 | 15-Jan-25 |
| A4850 | PCC Blinding Layer 9th Floor | 7 | 13-Aug-24 A | 20-Aug-24 A | 02-Apr-24 | 09-Apr-24 |
| A4860 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 13-Aug-24 A | 20-Aug-24 A | 02-Apr-24 | 09-Apr-24 |
| A4870 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 20-Aug-24 A | 22-Aug-24 A | 09-Apr-24 | 11-Apr-24 |
| A4880 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 22-Aug-24 A | 23-Aug-24 A | 11-Apr-24 | 12-Apr-24 |
| A4890 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 23-Aug-24 A | 30-Aug-24 A | 13-Apr-24 | 20-Apr-24 |
| A4900 | Formwork Stripping & Removal Section 1/4 | 3 | 30-Aug-24 A | 02-Sep-24 A | 22-Apr-24 | 24-Apr-24 |
| A4910 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 24-Aug-24 A | 31-Aug-24 A | 06-May-24 | 13-May-24 |
| A4920 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 31-Aug-24 A | 03-Sep-24 A | 14-May-24 | 16-May-24 |
| A4930 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 03-Aug-24 A | 05-Aug-24 A | 16-May-24 | 17-May-24 |
| A4940 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 05-Aug-24 A | 13-Aug-24 A | 17-May-24 | 25-May-24 |
| A4950 | Formwork Stripping & Removal Section 2/4 | 3 | 13-Aug-24 A | 15-Aug-24 A | 25-May-24 | 29-May-24 |
| A4960 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 06-Aug-24 A | 13-Aug-24 A | 15-Jun-24 | 22-Jun-24 |
| A4970 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 13-Aug-24 A | 16-Aug-24 A | 22-Jun-24 | 25-Jun-24 |
| A4980 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 16-Aug-24 A | 17-Aug-24 A | 26-Jun-24 | 27-Jun-24 |
| A4990 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 17-Aug-24 A | 26-Aug-24 A | 27-Jun-24 | 05-Jul-24 |
| A5000 | Formwork Stripping & Removal Section 3/4 | 3 | 26-Aug-24 A | 28-Aug-24 A | 05-Jul-24 | 08-Jul-24 |
| A5010 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 19-Aug-24 A | 26-Aug-24 A | 19-Jul-24 | 26-Jul-24 |
| A5020 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 26-Aug-24 A | 28-Aug-24 A | 26-Jul-24 | 29-Jul-24 |
| A5030 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 28-Aug-24 A | 29-Aug-24 A | 29-Jul-24 | 30-Jul-24 |
| A5040 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 29-Aug-24 A | 06-Sep-24 A | 31-Jul-24 | 07-Aug-24 |
| A5050 | Formwork Stripping & Removal Section 4/4 | 3 | 06-Sep-24 A | 09-Sep-24 A | 08-Aug-24 | 10-Aug-24 |
| A5060 | Brickwork & Masonry Partition Walls 9th Floor | 40 | 09-Sep-24 A | 25-Oct-24 A | 10-Aug-24 | 26-Sep-24 |
| A5070 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 9th F | 50 | 25-Oct-24 A | 23-Dec-24 A | 26-Sep-24 | 23-Nov-24 |
| A5080 | Floor Finishes (Tiles/Marble/Screed) 9th Floor [Basement (Parki | 45 | 23-Dec-24 A | 13-Feb-25 A | 23-Nov-24 | 15-Jan-25 |
| LAB CEP.PHASE2.10F 10TH FLOOR RESIDENTIAL APPARTMEN | | 185 | 02-Sep-24 A | 05-Apr-25 A | 24-Apr-24 | 06-Feb-25 |
| A5090 | PCC Blinding Layer 10th Floor | 7 | 02-Sep-24 A | 09-Sep-24 A | 24-Apr-24 | 02-May-24 |
| A5100 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 02-Sep-24 A | 09-Sep-24 A | 24-Apr-24 | 01-May-24 |
| A5110 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 09-Sep-24 A | 11-Sep-24 A | 01-May-24 | 04-May-24 |
| A5120 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 11-Sep-24 A | 12-Sep-24 A | 04-May-24 | 06-May-24 |
| A5130 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 12-Sep-24 A | 19-Sep-24 A | 06-May-24 | 14-May-24 |
| A5140 | Formwork Stripping & Removal Section 1/4 | 3 | 19-Sep-24 A | 21-Sep-24 A | 14-May-24 | 16-May-24 |
| A1100 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 13-Sep-24 A | 20-Sep-24 A | 29-May-24 | 05-Jun-24 |
| A5160 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 20-Sep-24 A | 23-Sep-24 A | 05-Jun-24 | 07-Jun-24 |
| A5170 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 23-Sep-24 A | 24-Sep-24 A | 08-Jun-24 | 10-Jun-24 |
| A5180 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 24-Sep-24 A | 02-Oct-24 A | 10-Jun-24 | 18-Jun-24 |
| A5190 | Formwork Stripping & Removal Section 2/4 | 3 | 02-Oct-24 A | 04-Oct-24 A | 18-Jun-24 | 20-Jun-24 |
| A5200 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 25-Sep-24 A | 02-Oct-24 A | 08-Jul-24 | 15-Jul-24 |
| A5210 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 02-Oct-24 A | 05-Oct-24 A | 16-Jul-24 | 18-Jul-24 |
| A5220 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 05-Oct-24 A | 07-Oct-24 A | 18-Jul-24 | 19-Jul-24 |

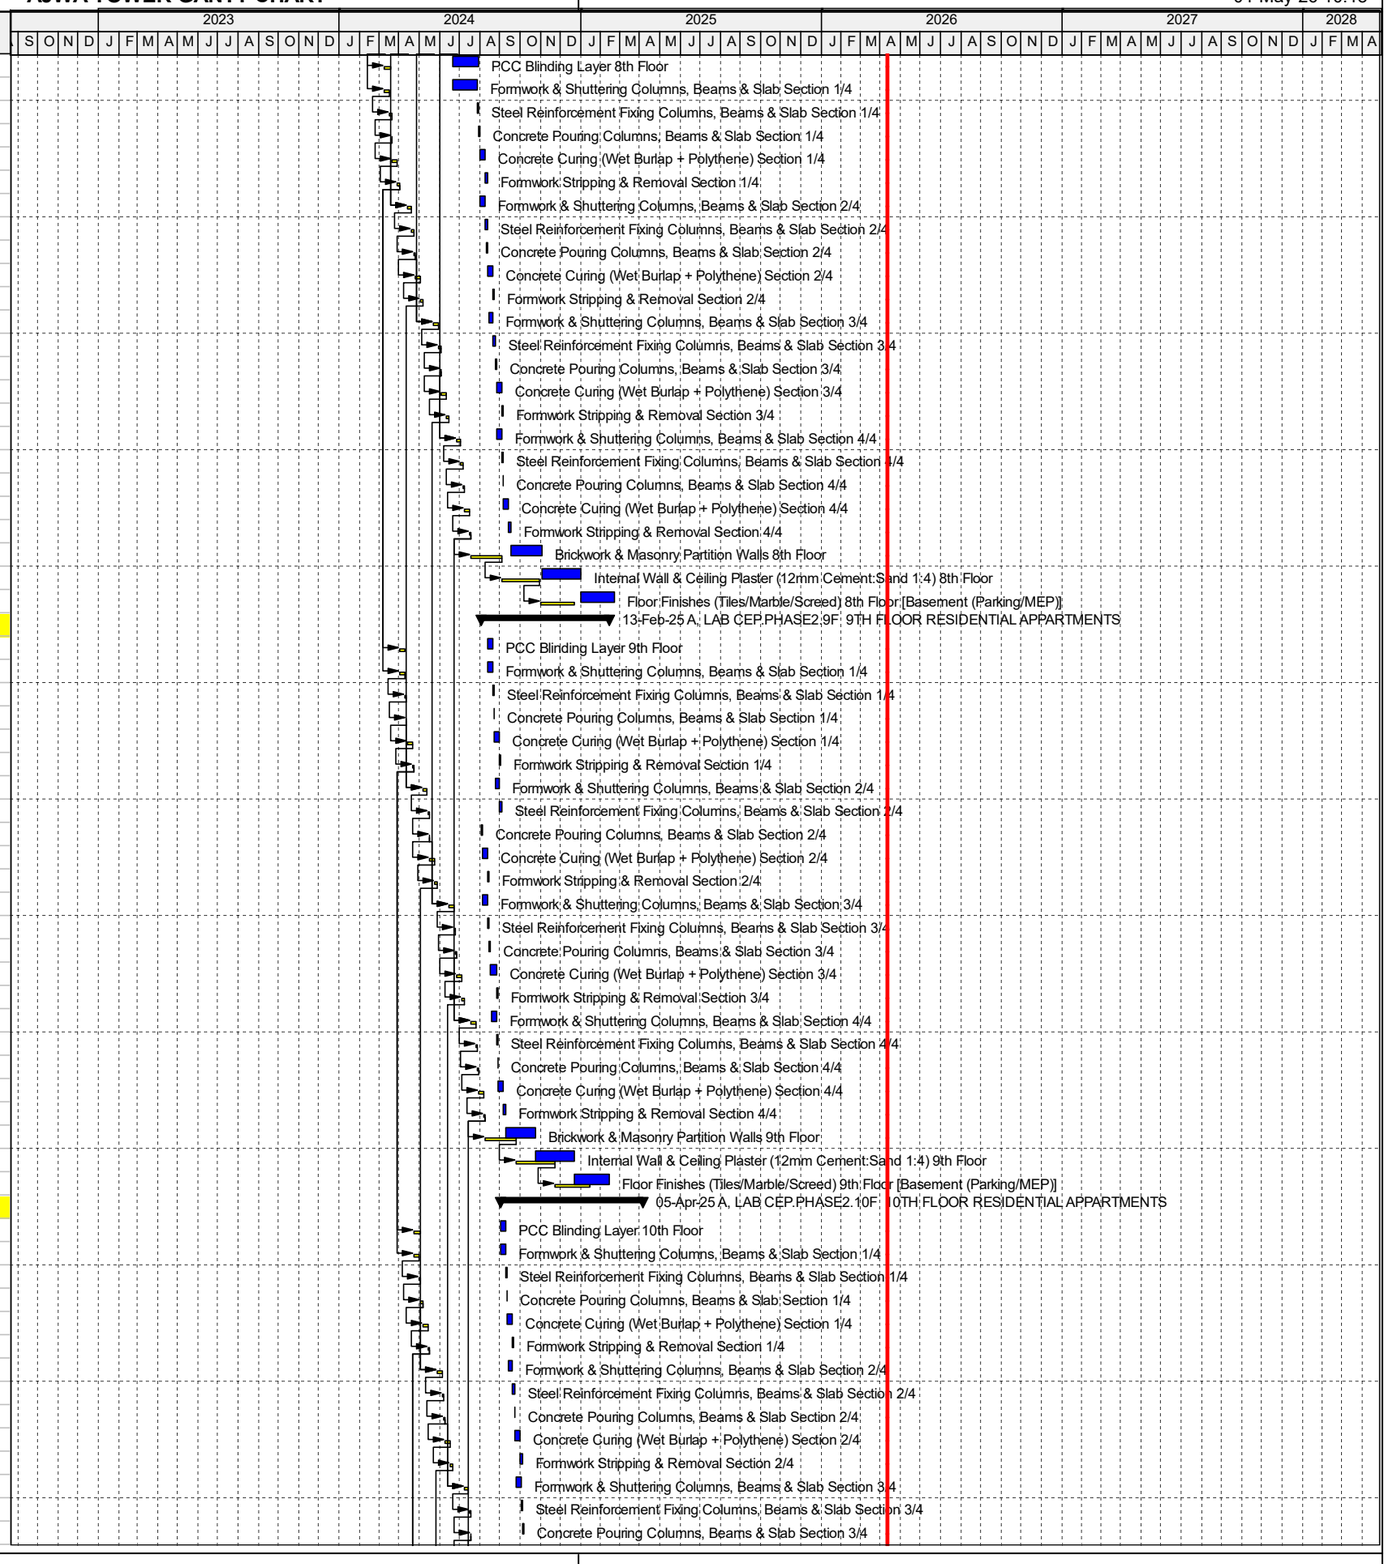




© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A5230 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 07-Oct-24 A | 15-Oct-24 A | 19-Jul-24 | 27-Jul-24 |
| A5240 | Formwork Stripping & Removal Section 3/4 | 3 | 15-Oct-24 A | 17-Oct-24 A | 27-Jul-24 | 31-Jul-24 |
| A5250 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 08-Oct-24 A | 15-Oct-24 A | 10-Aug-24 | 17-Aug-24 |
| A5260 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 15-Oct-24 A | 17-Oct-24 A | 17-Aug-24 | 21-Aug-24 |
| A5270 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 17-Oct-24 A | 18-Oct-24 A | 21-Aug-24 | 22-Aug-24 |
| A5280 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 18-Oct-24 A | 26-Oct-24 A | 22-Aug-24 | 30-Aug-24 |
| A5290 | Formwork Stripping & Removal Section 4/4 | 3 | 26-Oct-24 A | 30-Oct-24 A | 30-Aug-24 | 02-Sep-24 |
| A5300 | Brickwork & Masonry Partition Walls 10th Floor | 40 | 30-Oct-24 A | 16-Dec-24 A | 03-Sep-24 | 18-Oct-24 |
| A5310 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 10th | 50 | 16-Dec-24 A | 12-Feb-25 A | 19-Oct-24 | 16-Dec-24 |
| A5320 | Floor Finishes (Tiles/Marble/Screed) 10th Floor [Basement (Par | 45 | 12-Feb-25 A | 05-Apr-25 A | 17-Dec-24 | 06-Feb-25 |
| **LAB CEP.PHASE2.11F 11TH FLOOR RESIDENTIAL APPARTMEN** | | 205 | 21-Sep-24 A | 17-May-25 A | 17-May-24 | 01-Mar-25 |
| A5330 | PCC Blinding Layer 11th Floor | 7 | 21-Sep-24 A | 28-Sep-24 A | 17-May-24 | 24-May-24 |
| A5340 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 21-Sep-24 A | 28-Sep-24 A | 17-May-24 | 24-May-24 |
| A5350 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 28-Sep-24 A | 01-Oct-24 A | 24-May-24 | 27-May-24 |
| A5360 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 01-Oct-24 A | 02-Oct-24 A | 27-May-24 | 28-May-24 |
| A5370 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 02-Oct-24 A | 09-Oct-24 A | 29-May-24 | 05-Jun-24 |
| A5380 | Formwork Stripping & Removal Section 1/4 | 5 | 09-Oct-24 A | 14-Oct-24 A | 06-Jun-24 | 11-Jun-24 |
| A5390 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 03-Oct-24 A | 10-Oct-24 A | 20-Jun-24 | 27-Jun-24 |
| A5400 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 10-Oct-24 A | 12-Oct-24 A | 28-Jun-24 | 01-Jul-24 |
| A5410 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 12-Oct-24 A | 14-Oct-24 A | 01-Jul-24 | 02-Jul-24 |
| A5420 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 14-Oct-24 A | 22-Oct-24 A | 02-Jul-24 | 10-Jul-24 |
| A5430 | Formwork Stripping & Removal Section 2/4 | 3 | 22-Oct-24 A | 24-Oct-24 A | 10-Jul-24 | 13-Jul-24 |
| A5440 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 15-Oct-24 A | 22-Oct-24 A | 31-Jul-24 | 07-Aug-24 |
| A5450 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 22-Oct-24 A | 25-Oct-24 A | 07-Aug-24 | 09-Aug-24 |
| A5460 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 25-Oct-24 A | 26-Oct-24 A | 10-Aug-24 | 12-Aug-24 |
| A5470 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 26-Oct-24 A | 04-Nov-24 A | 12-Aug-24 | 20-Aug-24 |
| A5480 | Formwork Stripping & Removal Section 3/4 | 3 | 04-Nov-24 A | 06-Nov-24 A | 20-Aug-24 | 22-Aug-24 |
| A5490 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 28-Oct-24 A | 04-Nov-24 A | 03-Sep-24 | 10-Sep-24 |
| A5500 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 04-Nov-24 A | 06-Nov-24 A | 10-Sep-24 | 12-Sep-24 |
| A5510 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 06-Nov-24 A | 07-Nov-24 A | 12-Sep-24 | 13-Sep-24 |
| A5520 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 07-Nov-24 A | 15-Nov-24 A | 14-Sep-24 | 21-Sep-24 |
| A5530 | Formwork Stripping & Removal Section 4/4 | 3 | 15-Nov-24 A | 19-Nov-24 A | 23-Sep-24 | 25-Sep-24 |
| A5540 | Brickwork & Masonry Partition Walls 11th Floor | 40 | 06-Dec-24 A | 21-Jan-25 A | 25-Sep-24 | 11-Nov-24 |
| A5550 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 11th I | 50 | 21-Jan-25 A | 21-Mar-25 A | 11-Nov-24 | 08-Jan-25 |
| A5560 | Floor Finishes (Tiles/Marble/Screed) 11th Floor [Basement (Parl | 45 | 27-Mar-25 A | 17-May-25 A | 08-Jan-25 | 01-Mar-25 |
| **LAB CEP.PHASE2.12F 12TH FLOOR RESIDENTIAL APPARTMEN** | | 210 | 14-Oct-24 A | 24-Jun-25 A | 12-Jun-24 | 24-Mar-25 |
| A5570 | PCC Blinding Layer 12th Floor | 7 | 14-Oct-24 A | 21-Oct-24 A | 12-Jun-24 | 19-Jun-24 |
| A5580 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 21-Oct-24 A | 28-Oct-24 A | 12-Jun-24 | 19-Jun-24 |
| A5590 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 28-Oct-24 A | 30-Oct-24 A | 19-Jun-24 | 21-Jun-24 |
| A5600 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 30-Oct-24 A | 31-Oct-24 A | 21-Jun-24 | 22-Jun-24 |
| A5610 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 31-Oct-24 A | 09-Nov-24 A | 24-Jun-24 | 01-Jul-24 |
| A5620 | Formwork Stripping & Removal Section 1/4 | 3 | 09-Nov-24 A | 12-Nov-24 A | 02-Jul-24 | 04-Jul-24 |
| A5630 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 02-Nov-24 A | 09-Nov-24 A | 13-Jul-24 | 20-Jul-24 |
| A5640 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 09-Nov-24 A | 12-Nov-24 A | 20-Jul-24 | 23-Jul-24 |
| A5650 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 12-Nov-24 A | 13-Nov-24 A | 24-Jul-24 | 25-Jul-24 |
| A5660 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 13-Nov-24 A | 20-Nov-24 A | 25-Jul-24 | 02-Aug-24 |
| A5670 | Formwork Stripping & Removal Section 2/4 | 3 | 20-Nov-24 A | 22-Nov-24 A | 02-Aug-24 | 05-Aug-24 |
| A5680 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 22-Nov-24 A | 29-Nov-24 A | 22-Aug-24 | 29-Aug-24 |
| A5690 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 29-Nov-24 A | 02-Dec-24 A | 30-Aug-24 | 02-Sep-24 |
| A5700 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 02-Dec-24 A | 03-Dec-24 A | 02-Sep-24 | 03-Sep-24 |
| A5710 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 03-Dec-24 A | 10-Dec-24 A | 03-Sep-24 | 11-Sep-24 |
| A5720 | Formwork Stripping & Removal Section 3/4 | 3 | 10-Dec-24 A | 12-Dec-24 A | 11-Sep-24 | 14-Sep-24 |
| A5730 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 04-Dec-24 A | 11-Dec-24 A | 25-Sep-24 | 02-Oct-24 |
| A5740 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 11-Dec-24 A | 13-Dec-24 A | 02-Oct-24 | 05-Oct-24 |
| A5750 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 13-Dec-24 A | 14-Dec-24 A | 05-Oct-24 | 07-Oct-24 |
| A5760 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 14-Dec-24 A | 23-Dec-24 A | 07-Oct-24 | 15-Oct-24 |
| A5770 | Formwork Stripping & Removal Section 4/4 | 3 | 23-Dec-24 A | 25-Dec-24 A | 15-Oct-24 | 17-Oct-24 |
| A5780 | Brickwork & Masonry Partition Walls 12th Floor | 40 | 11-Jan-25 A | 26-Feb-25 A | 18-Oct-24 | 03-Dec-24 |
| A5790 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 12th | 50 | 26-Feb-25 A | 24-Apr-25 A | 04-Dec-24 | 30-Jan-25 |
| A5800 | Floor Finishes (Tiles/Marble/Screed) 12th Floor [Basement (Par | 45 | 24-Apr-25 A | 24-Jun-25 A | 31-Jan-25 | 24-Mar-25 |
| **LAB CEP.PHASE2.13F 13TH FLOOR HOTEL** | | 203 | 12-Nov-24 A | 05-Jul-25 A | 04-Jul-24 | 12-Apr-25 |
| A5810 | PCC Blinding Layer 13th Floor | 7 | 12-Nov-24 A | 19-Nov-24 A | 04-Jul-24 | 12-Jul-24 |
| A5820 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 12-Nov-24 A | 19-Nov-24 A | 04-Jul-24 | 11-Jul-24 |
| A5830 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 19-Nov-24 A | 21-Nov-24 A | 11-Jul-24 | 15-Jul-24 |

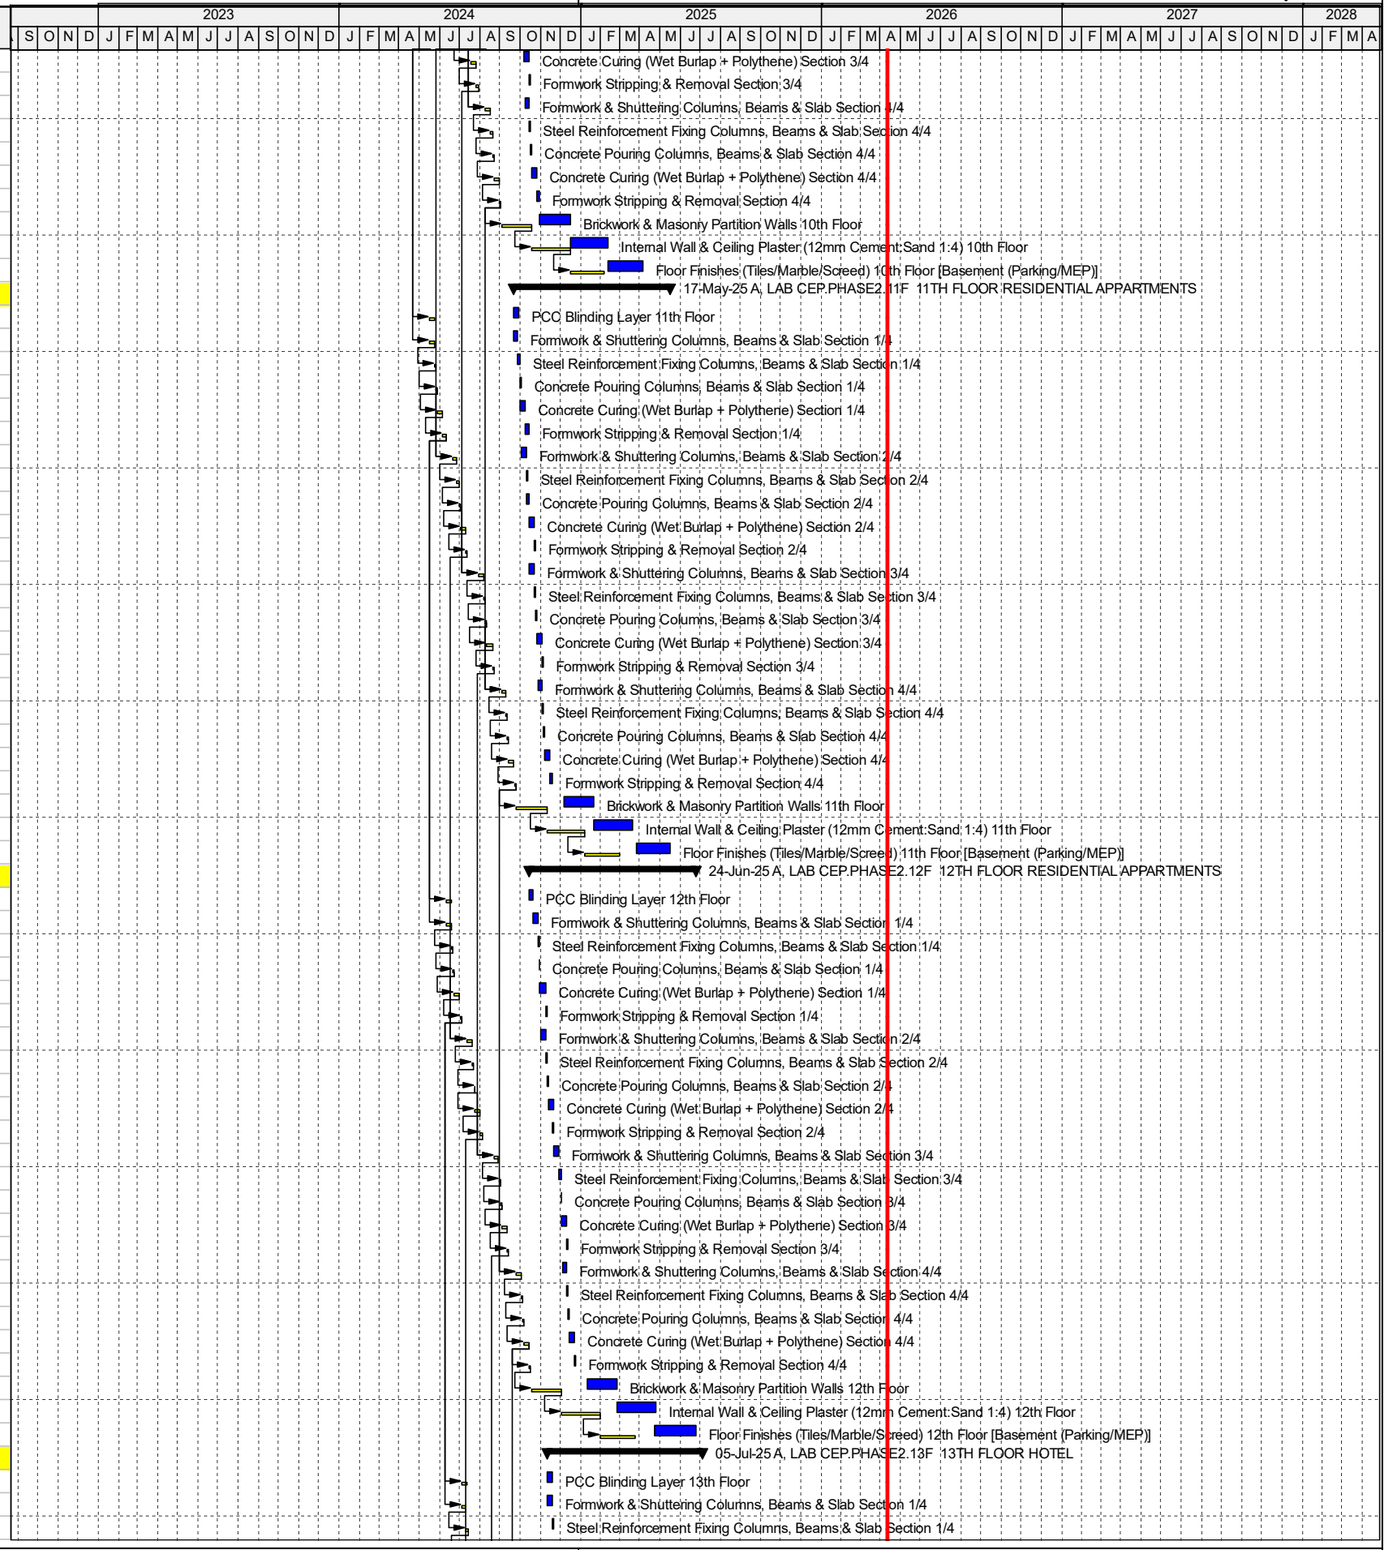





© Oracle Corporation

CEM LAB CEP 7112,7104,7135

# AJWA TOWER GANTT CHART

04-May-26 10:18

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A5840 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 21-Nov-24 A | 22-Nov-24 A | 15-Jul-24 | 16-Jul-24 |
| A5850 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 22-Nov-24 A | 29-Nov-24 A | 16-Jul-24 | 24-Jul-24 |
| A5860 | Formwork Stripping & Removal Section 1/4 | 3 | 29-Nov-24 A | 02-Dec-24 A | 24-Jul-24 | 26-Jul-24 |
| A5870 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 23-Nov-24 A | 30-Nov-24 A | 05-Aug-24 | 12-Aug-24 |
| A5880 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 30-Nov-24 A | 03-Dec-24 A | 13-Aug-24 | 15-Aug-24 |
| A5890 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 03-Dec-24 A | 04-Dec-24 A | 15-Aug-24 | 16-Aug-24 |
| A5900 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 04-Dec-24 A | 12-Dec-24 A | 16-Aug-24 | 24-Aug-24 |
| A5910 | Formwork Stripping & Removal Section 2/4 | 3 | 12-Dec-24 A | 14-Dec-24 A | 24-Aug-24 | 28-Aug-24 |
| A5920 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 05-Dec-24 A | 12-Dec-24 A | 14-Sep-24 | 21-Sep-24 |
| A5930 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 12-Dec-24 A | 16-Dec-24 A | 21-Sep-24 | 24-Sep-24 |
| A5940 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 16-Dec-24 A | 17-Dec-24 A | 25-Sep-24 | 26-Sep-24 |
| A5950 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 17-Dec-24 A | 25-Dec-24 A | 26-Sep-24 | 04-Oct-24 |
| A5960 | Formwork Stripping & Removal Section 3/4 | 3 | 25-Dec-24 A | 27-Dec-24 A | 04-Oct-24 | 07-Oct-24 |
| A5970 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 18-Dec-24 A | 25-Dec-24 A | 15-Oct-24 | 22-Oct-24 |
| A5980 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 25-Dec-24 A | 27-Dec-24 A | 22-Oct-24 | 25-Oct-24 |
| A5990 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 27-Dec-24 A | 28-Dec-24 A | 25-Oct-24 | 26-Oct-24 |
| A6000 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 28-Dec-24 A | 06-Jan-25 A | 26-Oct-24 | 04-Nov-24 |
| A6010 | Formwork Stripping & Removal Section 4/4 | 3 | 06-Jan-25 A | 09-Jan-25 A | 04-Nov-24 | 06-Nov-24 |
| A6020 | Brickwork & Masonry Partition Walls 13th Floor | 40 | 27-Jan-25 A | 13-Mar-25 A | 07-Nov-24 | 23-Dec-24 |
| A6030 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 13th | 50 | 13-Mar-25 A | 09-May-25 A | 24-Dec-24 | 19-Feb-25 |
| A6040 | Floor Finishes (Tiles/Marble/Screed) 13th Floor [Basement (Par | 45 | 15-May-25 A | 05-Jul-25 A | 20-Feb-25 | 12-Apr-25 |
| **LAB CEP.PHASE2.14F 14TH FLOOR HOTEL** | | 236 | 02-Dec-24 A | 02-Sep-25 A | 27-Jul-24 | 06-May-25 |
| A6050 | PCC Blinding Layer 14th Floor | 7 | 02-Dec-24 A | 09-Dec-24 A | 27-Jul-24 | 03-Aug-24 |
| A6060 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 02-Dec-24 A | 09-Dec-24 A | 27-Jul-24 | 03-Aug-24 |
| A6070 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 09-Dec-24 A | 11-Dec-24 A | 03-Aug-24 | 06-Aug-24 |
| A6080 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 01-Jan-25 A | 02-Jan-25 A | 06-Aug-24 | 07-Aug-24 |
| A6090 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 02-Jan-25 A | 10-Jan-25 A | 08-Aug-24 | 15-Aug-24 |
| A6100 | Formwork Stripping & Removal Section 1/4 | 3 | 10-Jan-25 A | 13-Jan-25 A | 16-Aug-24 | 19-Aug-24 |
| A6110 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 03-Jan-25 A | 10-Jan-25 A | 28-Aug-24 | 04-Sep-24 |
| A6120 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 10-Jan-25 A | 14-Jan-25 A | 04-Sep-24 | 06-Sep-24 |
| A6130 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 14-Jan-25 A | 15-Jan-25 A | 07-Sep-24 | 09-Sep-24 |
| A6140 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 15-Jan-25 A | 23-Jan-25 A | 09-Sep-24 | 17-Sep-24 |
| A6150 | Formwork Stripping & Removal Section 2/4 | 3 | 23-Jan-25 A | 25-Jan-25 A | 17-Sep-24 | 19-Sep-24 |
| A6160 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 16-Jan-25 A | 23-Jan-25 A | 07-Oct-24 | 14-Oct-24 |
| A6170 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 23-Jan-25 A | 25-Jan-25 A | 15-Oct-24 | 17-Oct-24 |
| A6180 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 25-Jan-25 A | 27-Jan-25 A | 17-Oct-24 | 18-Oct-24 |
| A6190 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 27-Jan-25 A | 04-Feb-25 A | 18-Oct-24 | 26-Oct-24 |
| A6200 | Formwork Stripping & Removal Section 3/4 | 3 | 04-Feb-25 A | 07-Feb-25 A | 26-Oct-24 | 30-Oct-24 |
| A6210 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 28-Jan-25 A | 04-Feb-25 A | 07-Nov-24 | 14-Nov-24 |
| A6220 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 04-Feb-25 A | 06-Feb-25 A | 14-Nov-24 | 16-Nov-24 |
| A6230 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 06-Feb-25 A | 07-Feb-25 A | 16-Nov-24 | 18-Nov-24 |
| A6240 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 07-Feb-25 A | 15-Feb-25 A | 19-Nov-24 | 26-Nov-24 |
| A6250 | Formwork Stripping & Removal Section 4/4 | 3 | 15-Feb-25 A | 18-Feb-25 A | 27-Nov-24 | 29-Nov-24 |
| A6260 | Brickwork & Masonry Partition Walls 14th Floor | 40 | 04-Mar-25 A | 18-Apr-25 A | 29-Nov-24 | 15-Jan-25 |
| A6270 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 14th | 50 | 02-May-25 A | 28-Jun-25 A | 15-Jan-25 | 14-Mar-25 |
| A6280 | Floor Finishes (Tiles/Marble/Screed) 14th Floor [Basement (Par | 45 | 12-Jul-25 A | 02-Sep-25 A | 14-Mar-25 | 06-May-25 |
| **LAB CEP.PHASE2.15F 15TH FLOOR HOTEL** | | 211 | 13-Jan-25 A | 15-Sep-25 A | 19-Aug-24 | 28-May-25 |
| A6290 | PCC Blinding Layer 15th Floor | 7 | 13-Jan-25 A | 20-Jan-25 A | 19-Aug-24 | 27-Aug-24 |
| A6300 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 13-Jan-25 A | 20-Jan-25 A | 19-Aug-24 | 26-Aug-24 |
| A6310 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 20-Jan-25 A | 22-Jan-25 A | 26-Aug-24 | 29-Aug-24 |
| A6320 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 29-Jan-25 A | 30-Jan-25 A | 29-Aug-24 | 30-Aug-24 |
| A6330 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 30-Jan-25 A | 07-Feb-25 A | 30-Aug-24 | 07-Sep-24 |
| A6340 | Formwork Stripping & Removal Section 1/4 | 3 | 07-Feb-25 A | 10-Feb-25 A | 07-Sep-24 | 10-Sep-24 |
| A6350 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 31-Jan-25 A | 07-Feb-25 A | 19-Sep-24 | 26-Sep-24 |
| A6360 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 07-Feb-25 A | 11-Feb-25 A | 27-Sep-24 | 30-Sep-24 |
| A6370 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 18-Feb-25 A | 19-Feb-25 A | 30-Sep-24 | 01-Oct-24 |
| A6380 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 19-Feb-25 A | 27-Feb-25 A | 01-Oct-24 | 09-Oct-24 |
| A6390 | Formwork Stripping & Removal Section 2/4 | 3 | 27-Feb-25 A | 01-Mar-25 A | 09-Oct-24 | 12-Oct-24 |
| A6400 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 20-Feb-25 A | 27-Feb-25 A | 30-Oct-24 | 06-Nov-24 |
| A1100 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 27-Feb-25 A | 03-Mar-25 A | 06-Nov-24 | 08-Nov-24 |
| A6420 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 10-Mar-25 A | 11-Mar-25 A | 09-Nov-24 | 11-Nov-24 |
| A6430 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 11-Mar-25 A | 19-Mar-25 A | 11-Nov-24 | 19-Nov-24 |
| A6440 | Formwork Stripping & Removal Section 3/4 | 3 | 19-Mar-25 A | 21-Mar-25 A | 19-Nov-24 | 21-Nov-24 |
| A6450 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 12-Mar-25 A | 19-Mar-25 A | 29-Nov-24 | 06-Dec-24 |

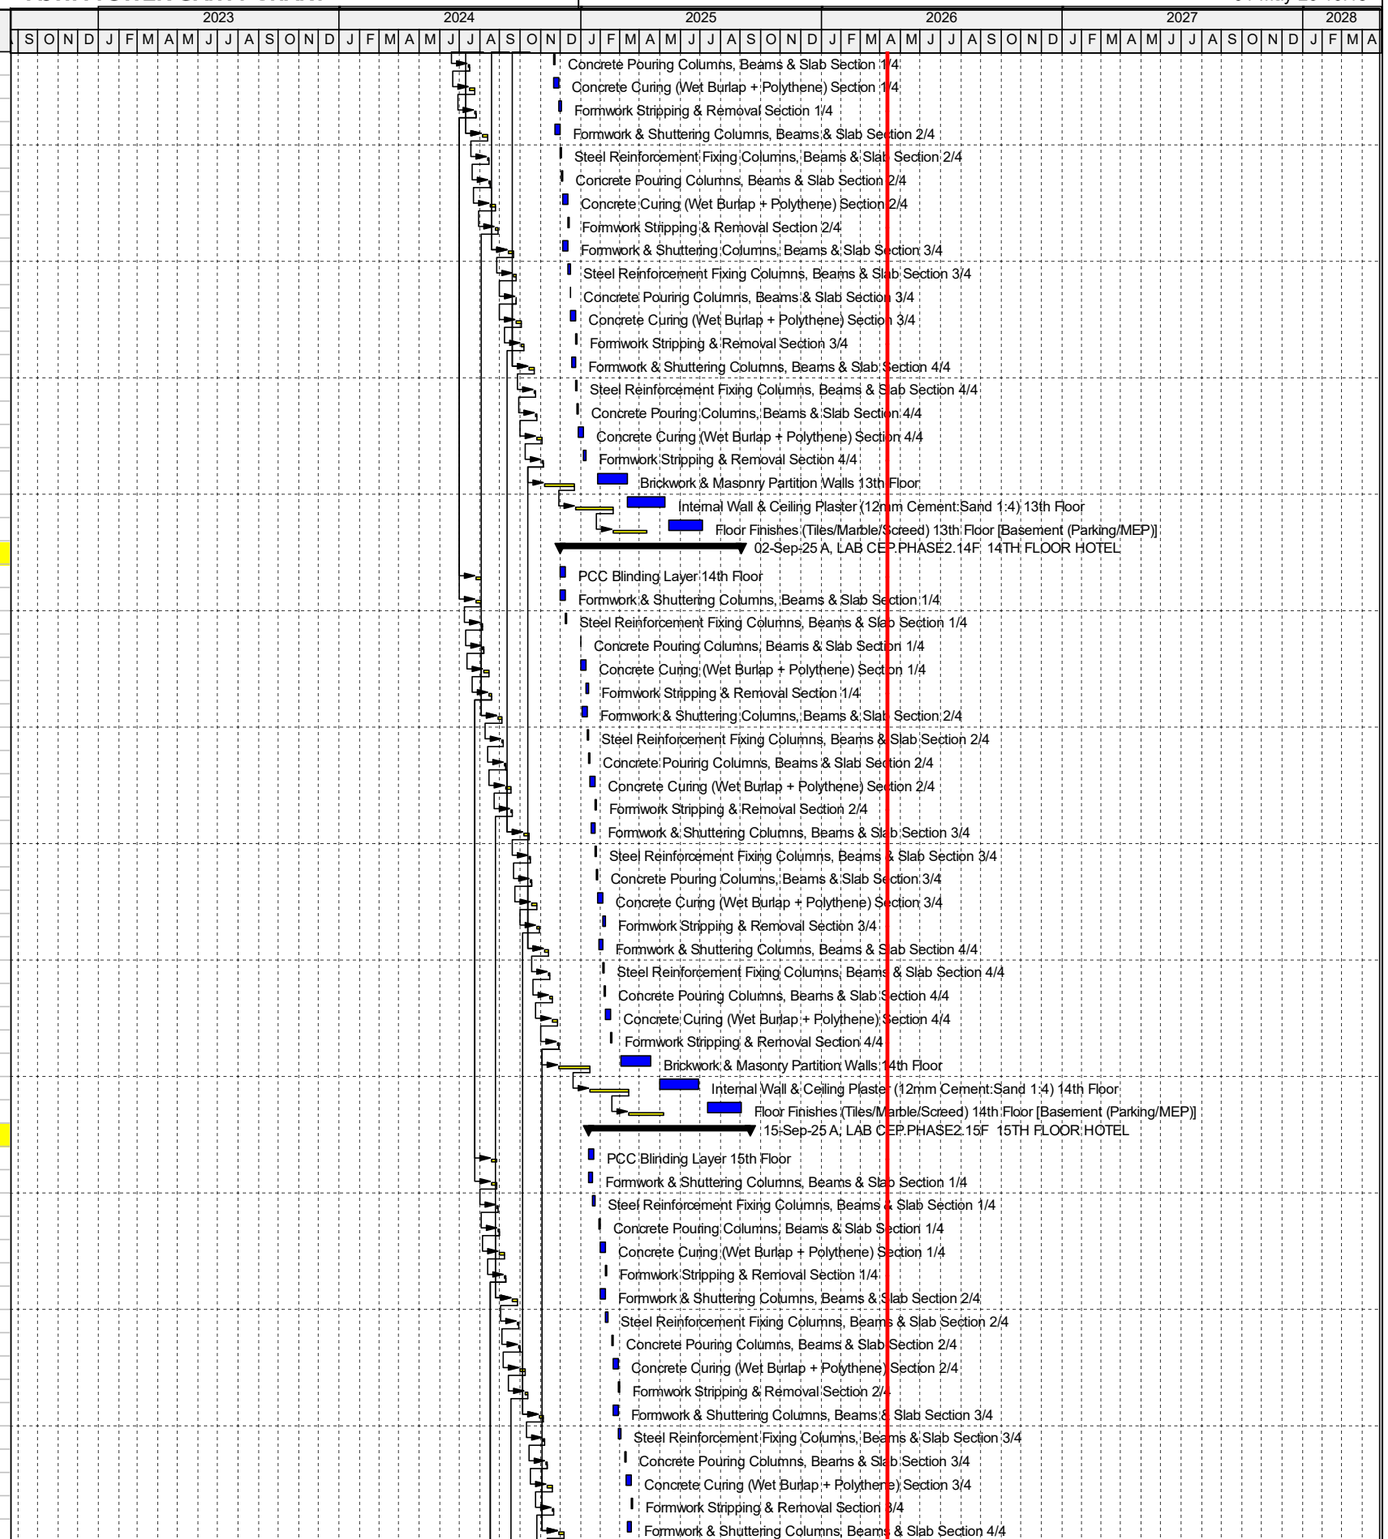



Actual Level of Effort | Actual Work | Critical Remaining Work
Primary Baseline | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A6460 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 19-Mar-25 A | 22-Mar-25 A | 06-Dec-24 | 10-Dec-24 |
| A6470 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 29-Mar-25 A | 31-Mar-25 A | 10-Dec-24 | 11-Dec-24 |
| A6480 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 31-Mar-25 A | 08-Apr-25 A | 11-Dec-24 | 19-Dec-24 |
| A6490 | Formwork Stripping & Removal Section 4/4 | 3 | 08-Apr-25 A | 10-Apr-25 A | 19-Dec-24 | 21-Dec-24 |
| A6500 | Brickwork & Masonry Partition Walls 15th Floor | 40 | 10-Apr-25 A | 27-May-25 A | 23-Dec-24 | 06-Feb-25 |
| A6510 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 15th | 50 | 27-May-25 A | 24-Jul-25 A | 07-Feb-25 | 05-Apr-25 |
| A6520 | Floor Finishes (Tiles/Marble/Screed) 15th Floor [Basement (Par | 45 | 24-Jul-25 A | 15-Sep-25 A | 07-Apr-25 | 28-May-25 |
| **LAB CEP.PHASE2.16F 16TH FLOOR HOTEL** | | 238 | 01-Mar-25 A | 03-Dec-25 A | 11-Sep-24 | 20-Jun-25 |
| A6530 | PCC Blinding Layer 16th Floor | 7 | 01-Mar-25 A | 08-Mar-25 A | 11-Sep-24 | 18-Sep-24 |
| A6540 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 01-Mar-25 A | 08-Mar-25 A | 11-Sep-24 | 18-Sep-24 |
| A6550 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 08-Mar-25 A | 11-Mar-25 A | 18-Sep-24 | 20-Sep-24 |
| A6560 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 18-Mar-25 A | 19-Mar-25 A | 20-Sep-24 | 21-Sep-24 |
| A6570 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 19-Mar-25 A | 27-Mar-25 A | 23-Sep-24 | 30-Sep-24 |
| A6580 | Formwork Stripping & Removal Section 1/4 | 3 | 27-Mar-25 A | 29-Mar-25 A | 01-Oct-24 | 03-Oct-24 |
| A6590 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 20-Mar-25 A | 27-Mar-25 A | 12-Oct-24 | 19-Oct-24 |
| A6600 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 01-Apr-25 A | 03-Apr-25 A | 19-Oct-24 | 22-Oct-24 |
| A6610 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 10-Apr-25 A | 11-Apr-25 A | 23-Oct-24 | 24-Oct-24 |
| A6620 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 11-Apr-25 A | 19-Apr-25 A | 24-Oct-24 | 01-Nov-24 |
| A6630 | Formwork Stripping & Removal Section 2/4 | 3 | 19-Apr-25 A | 22-Apr-25 A | 01-Nov-24 | 04-Nov-24 |
| A6640 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 12-Apr-25 A | 19-Apr-25 A | 21-Nov-24 | 28-Nov-24 |
| A6650 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 19-Apr-25 A | 23-Apr-25 A | 29-Nov-24 | 02-Dec-24 |
| A6660 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 26-May-25 A | 27-May-25 A | 02-Dec-24 | 03-Dec-24 |
| A6670 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 27-May-25 A | 04-Jun-25 A | 03-Dec-24 | 11-Dec-24 |
| A6680 | Formwork Stripping & Removal Section 3/4 | 7 | 04-Jun-25 A | 12-Jun-25 A | 11-Dec-24 | 19-Dec-24 |
| A6690 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 28-May-25 A | 04-Jun-25 A | 23-Dec-24 | 30-Dec-24 |
| A6700 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 10-Jun-25 A | 12-Jun-25 A | 30-Dec-24 | 01-Jan-25 |
| A6710 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 17-Jun-25 A | 18-Jun-25 A | 01-Jan-25 | 02-Jan-25 |
| A6720 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 18-Jun-25 A | 26-Jun-25 A | 03-Jan-25 | 10-Jan-25 |
| A6730 | Formwork Stripping & Removal Section 4/4 | 3 | 26-Jun-25 A | 28-Jun-25 A | 11-Jan-25 | 14-Jan-25 |
| A6740 | Brickwork & Masonry Partition Walls 16th Floor | 40 | 28-Jun-25 A | 14-Aug-25 A | 14-Jan-25 | 01-Mar-25 |
| A6750 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 16th | 50 | 14-Aug-25 A | 11-Oct-25 A | 01-Mar-25 | 29-Apr-25 |
| A6760 | Floor Finishes (Tiles/Marble/Screed) 16th Floor [Basement (Par | 45 | 11-Oct-25 A | 03-Dec-25 A | 29-Apr-25 | 20-Jun-25 |
| **LAB CEP.PHASE2.17F 17TH FLOOR HOTEL** | | 269 | 15-Apr-25 A | 21-Feb-26 A | 03-Oct-24 | 12-Jul-25 |
| A6770 | PCC Blinding Layer 17th Floor | 7 | 15-Apr-25 A | 22-Apr-25 A | 03-Oct-24 | 11-Oct-24 |
| A6780 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 6 | 15-Apr-25 A | 22-Apr-25 A | 03-Oct-24 | 10-Oct-24 |
| A6790 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 22-Apr-25 A | 24-Apr-25 A | 10-Oct-24 | 14-Oct-24 |
| A6800 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 26-May-25 A | 27-May-25 A | 14-Oct-24 | 15-Oct-24 |
| A6810 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 27-May-25 A | 04-Jun-25 A | 15-Oct-24 | 23-Oct-24 |
| A6820 | Formwork Stripping & Removal Section 1/4 | 3 | 04-Jun-25 A | 06-Jun-25 A | 23-Oct-24 | 25-Oct-24 |
| A6830 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 6 | 28-May-25 A | 04-Jun-25 A | 04-Nov-24 | 11-Nov-24 |
| A6840 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 04-Jun-25 A | 07-Jun-25 A | 12-Nov-24 | 14-Nov-24 |
| A6850 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 20-Jun-25 A | 21-Jun-25 A | 14-Nov-24 | 15-Nov-24 |
| A6860 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 21-Jun-25 A | 30-Jun-25 A | 15-Nov-24 | 23-Nov-24 |
| A6870 | Formwork Stripping & Removal Section 2/4 | 3 | 30-Jun-25 A | 02-Jul-25 A | 23-Nov-24 | 27-Nov-24 |
| A6880 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 6 | 23-Jun-25 A | 30-Jun-25 A | 19-Dec-24 | 26-Dec-24 |
| A6890 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 30-Jun-25 A | 03-Jul-25 A | 27-Dec-24 | 30-Dec-24 |
| A6900 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 15-Aug-25 A | 16-Aug-25 A | 30-Dec-24 | 31-Dec-24 |
| A6910 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 16-Aug-25 A | 25-Aug-25 A | 31-Dec-24 | 08-Jan-25 |
| A6920 | Formwork Stripping & Removal Section 3/4 | 3 | 25-Aug-25 A | 27-Aug-25 A | 08-Jan-25 | 11-Jan-25 |
| A6930 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 6 | 18-Aug-25 A | 25-Aug-25 A | 14-Jan-25 | 21-Jan-25 |
| A6940 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 25-Aug-25 A | 28-Aug-25 A | 21-Jan-25 | 24-Jan-25 |
| A6950 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 05-Sep-25 A | 06-Sep-25 A | 24-Jan-25 | 25-Jan-25 |
| A6960 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 06-Sep-25 A | 15-Sep-25 A | 25-Jan-25 | 03-Feb-25 |
| A6970 | Formwork Stripping & Removal Section 4/4 | 3 | 15-Sep-25 A | 17-Sep-25 A | 03-Feb-25 | 05-Feb-25 |
| A6980 | Brickwork & Masonry Partition Walls 17th Floor | 40 | 17-Sep-25 A | 03-Nov-25 A | 06-Feb-25 | 24-Mar-25 |
| A6990 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 17th | 50 | 03-Nov-25 A | 31-Dec-25 A | 25-Mar-25 | 21-May-25 |
| A1100 | Floor Finishes (Tiles/Marble/Screed) 17th Floor [Basement (Par | 45 | 31-Dec-25 A | 21-Feb-26 A | 22-May-25 | 12-Jul-25 |
| **LAB CEP.PHASE2.18F 18TH FLOOR HOTEL** | | 216 | 15-Aug-25 A | 23-Apr-26 A | 26-Oct-24 | 04-Aug-25 |
| A7010 | PCC Blinding Layer 18th Floor | 6 | 15-Aug-25 A | 22-Aug-25 A | 26-Oct-24 | 02-Nov-24 |
| A7020 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 15-Aug-25 A | 20-Aug-25 A | 26-Oct-24 | 31-Oct-24 |
| A7030 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 20-Aug-25 A | 22-Aug-25 A | 01-Nov-24 | 04-Nov-24 |
| A7040 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 28-Aug-25 A | 29-Aug-25 A | 04-Nov-24 | 05-Nov-24 |
| A7050 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 29-Aug-25 A | 06-Sep-25 A | 05-Nov-24 | 13-Nov-24 |
| A7060 | Formwork Stripping & Removal Section 1/4 | 3 | 06-Sep-25 A | 09-Sep-25 A | 13-Nov-24 | 16-Nov-24 |

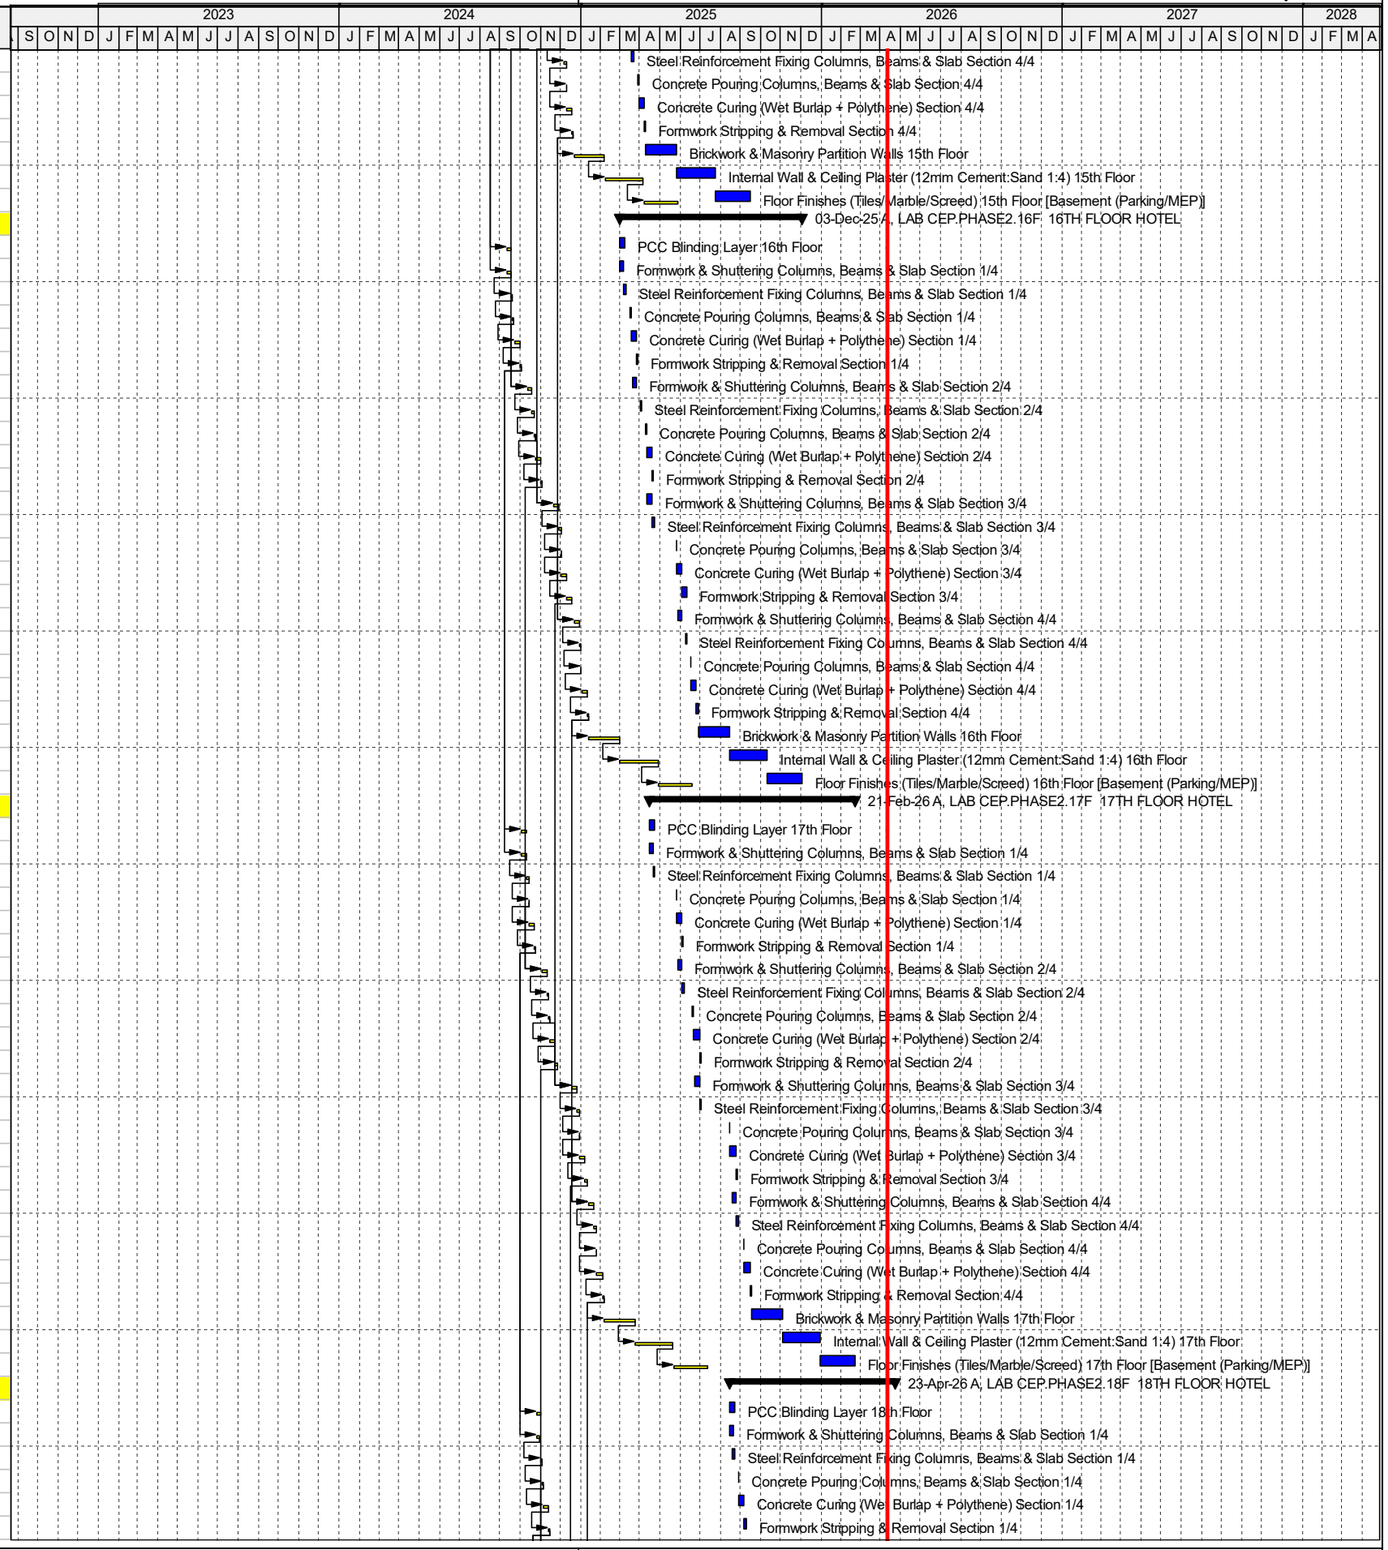


Actual Level of Effort | Actual Work | Critical Remaining Work

Primary Baseline | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A7070 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 5 | 30-Aug-25 A | 05-Sep-25 A | 27-Nov-24 | 03-Dec-24 |
| A7080 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 05-Sep-25 A | 08-Sep-25 A | 03-Dec-24 | 05-Dec-24 |
| A7090 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 20-Sep-25 A | 22-Sep-25 A | 05-Dec-24 | 06-Dec-24 |
| A7100 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 22-Sep-25 A | 30-Sep-25 A | 07-Dec-24 | 14-Dec-24 |
| A7110 | Formwork Stripping & Removal Section 2/4 | 3 | 30-Sep-25 A | 02-Oct-25 A | 16-Dec-24 | 18-Dec-24 |
| A7120 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 5 | 23-Sep-25 A | 29-Sep-25 A | 11-Jan-25 | 17-Jan-25 |
| A7130 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 29-Sep-25 A | 01-Oct-25 A | 17-Jan-25 | 20-Jan-25 |
| A7140 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 10-Oct-25 A | 11-Oct-25 A | 20-Jan-25 | 21-Jan-25 |
| A7150 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 11-Oct-25 A | 20-Oct-25 A | 22-Jan-25 | 29-Jan-25 |
| A7160 | Formwork Stripping & Removal Section 3/4 | 3 | 20-Oct-25 A | 22-Oct-25 A | 30-Jan-25 | 01-Feb-25 |
| A7170 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 5 | 13-Oct-25 A | 18-Oct-25 A | 06-Feb-25 | 11-Feb-25 |
| A7180 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 25-Oct-25 A | 28-Oct-25 A | 12-Feb-25 | 14-Feb-25 |
| A7190 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 05-Nov-25 A | 06-Nov-25 A | 14-Feb-25 | 15-Feb-25 |
| A7200 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 06-Nov-25 A | 14-Nov-25 A | 15-Feb-25 | 24-Feb-25 |
| A7210 | Formwork Stripping & Removal Section 4/4 | 3 | 14-Nov-25 A | 17-Nov-25 A | 24-Feb-25 | 27-Feb-25 |
| A7220 | Brickwork & Masonry Partition Walls 18th Floor | 40 | 17-Nov-25 A | 02-Jan-26 A | 27-Feb-25 | 15-Apr-25 |
| A7230 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 18th | 50 | 02-Jan-26 A | 02-Mar-26 A | 15-Apr-25 | 12-Jun-25 |
| A7240 | Floor Finishes (Tiles/Marble/Screed) 18th Floor [Basement (Par | 45 | 02-Mar-26 A | 23-Apr-26 A | 12-Jun-25 | 04-Aug-25 |
| LAB CEP.PHASE2.19F 19TH FLOOR HOTEL | | 314 | 20-May-25 A | 20-May-26 A | 16-Nov-24 | 21-Jul-25 |
| A7250 | PCC Blinding Layer 19th Floor | 6 | 15-Sep-25 A | 22-Sep-25 A | 16-Nov-24 | 23-Nov-24 |
| A7260 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 5 | 15-Sep-25 A | 19-Sep-25 A | 16-Nov-24 | 22-Nov-24 |
| A7270 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 01-Oct-25 A | 03-Oct-25 A | 22-Nov-24 | 25-Nov-24 |
| A7280 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 10-Oct-25 A | 11-Oct-25 A | 25-Nov-24 | 26-Nov-24 |
| A7290 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 11-Oct-25 A | 20-Oct-25 A | 27-Nov-24 | 04-Dec-24 |
| A7300 | Formwork Stripping & Removal Section 1/4 | 3 | 20-Oct-25 A | 22-Oct-25 A | 05-Dec-24 | 07-Dec-24 |
| A7310 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 5 | 13-Oct-25 A | 18-Oct-25 A | 18-Dec-24 | 24-Dec-24 |
| A7320 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 25-Oct-25 A | 28-Oct-25 A | 24-Dec-24 | 26-Dec-24 |
| A7330 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 10-Nov-25 A | 11-Nov-25 A | 27-Dec-24 | 28-Dec-24 |
| A7340 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 11-Nov-25 A | 19-Nov-25 A | 28-Dec-24 | 06-Jan-25 |
| A7350 | Formwork Stripping & Removal Section 2/4 | 3 | 19-Nov-25 A | 21-Nov-25 A | 06-Jan-25 | 08-Jan-25 |
| A7360 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 5 | 12-Nov-25 A | 18-Nov-25 A | 01-Feb-25 | 07-Feb-25 |
| A7370 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 02-Jan-26 A | 05-Jan-26 A | 07-Feb-25 | 10-Feb-25 |
| A7380 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 15-Jan-26 A | 16-Jan-26 A | 11-Feb-25 | 12-Feb-25 |
| A7390 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 16-Jan-26 A | 24-Jan-26 A | 12-Feb-25 | 20-Feb-25 |
| A7400 | Formwork Stripping & Removal Section 3/4 | 3 | 24-Jan-26 A | 27-Jan-26 A | 20-Feb-25 | 22-Feb-25 |
| A7410 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 5 | 17-Jan-26 A | 23-Jan-26 A | 27-Feb-25 | 05-Mar-25 |
| A7420 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 02-Feb-26 A | 04-Feb-26 A | 05-Mar-25 | 07-Mar-25 |
| A7430 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 16-Feb-26 A | 17-Feb-26 A | 07-Mar-25 | 08-Mar-25 |
| A7440 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 17-Feb-26 A | 25-Feb-26 A | 10-Mar-25 | 17-Mar-25 |
| A7450 | Formwork Stripping & Removal Section 4/4 | 3 | 25-Feb-26 A | 27-Feb-26 A | 18-Mar-25 | 20-Mar-25 |
| A7460 | Brickwork & Masonry Partition Walls 19th Floor | 30 | 27-Feb-26 A | 03-Apr-26 A | 20-Mar-25 | 24-Apr-25 |
| A7470 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 19th | 40 | 03-Apr-26 A | 20-May-26 A | 24-Apr-25 | 10-Jun-25 |
| A7480 | Floor Finishes (Tiles/Marble/Screed) 19th Floor [Basement (Par | 35 | 20-May-25 A | 28-Jun-25 A | 10-Jun-25 | 21-Jul-25 |
| LAB CEP.PHASE2.20F 20TH FLOOR ROOF | | 227 | 20-Oct-25 A | 10-Jul-26 | 07-Dec-24 | 05-Jul-25 |
| A7490 | PCC Blinding Layer 20th Floor | 6 | 20-Oct-25 A | 27-Oct-25 A | 07-Dec-24 | 14-Dec-24 |
| A7500 | Formwork & Shuttering Columns, Beams & Slab Section 1/4 | 4 | 20-Oct-25 A | 23-Oct-25 A | 07-Dec-24 | 12-Dec-24 |
| A7510 | Steel Reinforcement Fixing Columns, Beams & Slab Section 1 | 3 | 23-Oct-25 A | 27-Oct-25 A | 12-Dec-24 | 14-Dec-24 |
| A7520 | Concrete Pouring Columns, Beams & Slab Section 1/4 | 1 | 02-Jan-26 A | 03-Jan-26 A | 14-Dec-24 | 16-Dec-24 |
| A7530 | Concrete Curing (Wet Burlap + Polythene) Section 1/4 | 7 | 03-Jan-26 A | 12-Jan-26 A | 17-Dec-24 | 24-Dec-24 |
| A7540 | Formwork Stripping & Removal Section 1/4 | 3 | 12-Jan-26 A | 14-Jan-26 A | 25-Dec-24 | 27-Dec-24 |
| A7550 | Formwork & Shuttering Columns, Beams & Slab Section 2/4 | 4 | 05-Jan-26 A | 09-Jan-26 A | 08-Jan-25 | 13-Jan-25 |
| A7560 | Steel Reinforcement Fixing Columns, Beams & Slab Section 2 | 3 | 09-Jan-26 A | 12-Jan-26 A | 13-Jan-25 | 15-Jan-25 |
| A7570 | Concrete Pouring Columns, Beams & Slab Section 2/4 | 1 | 26-Jan-26 A | 27-Jan-26 A | 16-Jan-25 | 17-Jan-25 |
| A7580 | Concrete Curing (Wet Burlap + Polythene) Section 2/4 | 7 | 27-Jan-26 A | 04-Feb-26 A | 17-Jan-25 | 25-Jan-25 |
| A7590 | Formwork Stripping & Removal Section 2/4 | 3 | 04-Feb-26 A | 06-Feb-26 A | 25-Jan-25 | 28-Jan-25 |
| A7600 | Formwork & Shuttering Columns, Beams & Slab Section 3/4 | 4 | 28-Jan-26 A | 02-Feb-26 A | 22-Feb-25 | 27-Feb-25 |
| A7610 | Steel Reinforcement Fixing Columns, Beams & Slab Section 3 | 3 | 16-Feb-26 A | 18-Feb-26 A | 27-Feb-25 | 01-Mar-25 |
| A7620 | Concrete Pouring Columns, Beams & Slab Section 3/4 | 1 | 02-Mar-26 A | 03-Mar-26 A | 03-Mar-25 | 04-Mar-25 |
| A7630 | Concrete Curing (Wet Burlap + Polythene) Section 3/4 | 7 | 03-Mar-26 A | 11-Mar-26 A | 04-Mar-25 | 12-Mar-25 |
| A7640 | Formwork Stripping & Removal Section 3/4 | 3 | 11-Mar-26 A | 13-Mar-26 A | 12-Mar-25 | 14-Mar-25 |
| A7650 | Formwork & Shuttering Columns, Beams & Slab Section 4/4 | 4 | 04-Mar-26 A | 09-Mar-26 A | 20-Mar-25 | 25-Mar-25 |
| A7660 | Steel Reinforcement Fixing Columns, Beams & Slab Section 4 | 3 | 20-Mar-26 A | 23-Mar-26 A | 25-Mar-25 | 27-Mar-25 |
| A1100 | Concrete Pouring Columns, Beams & Slab Section 4/4 | 1 | 02-Apr-26 A | 03-Apr-26 A | 27-Mar-25 | 28-Mar-25 |
| A7680 | Concrete Curing (Wet Burlap + Polythene) Section 4/4 | 7 | 03-Apr-26 A | 11-Apr-26 A | 29-Mar-25 | 05-Apr-25 |




Actual Level of Effort | Actual Work | Critical Remaining Work


Primary Baseline | Remaining Work | ◆ Milestone



TASK filter: All Activities

© Oracle Corporation

| Activity ID | Activity Name | Original Duration | Start | Finish | BL Project Start | BL Project Finish |
|---|---|---|---|---|---|---|
| A7690 | Formwork Stripping & Removal Section 4/4 | 3 | 11-Apr-26 | 14-Apr-26 | 07-Apr-25 | 09-Apr-25 |
| A7700 | Brickwork & Masonry Partition Walls 20th Floor | 20 | 14-Apr-26 | 07-May-26 | 09-Apr-25 | 02-May-25 |
| A7710 | Internal Wall & Ceiling Plaster (12mm Cement:Sand 1:4) 20th | 30 | 07-May-26 | 11-Jun-26 | 02-May-25 | 06-Jun-25 |
| A7720 | Floor Finishes (Tiles/Marble/Screed) 20th Floor [Basement (Par | 25 | 11-Jun-26 | 10-Jul-26 | 06-Jun-25 | 05-Jul-25 |
| **LAB CEP.PHASE3 POST-CONSTRUCTION: MEP, FIN** | | 105 | 11-Jun-26 | 12-Oct-26 | 06-Jun-25 | 07-Oct-25 |
| **LAB CEP.PHASE3.MEP MEP WORKS** | | 28 | 11-Jun-26 | 13-Jul-26 | 06-Jun-25 | 08-Jul-25 |
| A7730 | Electrical Conduit, Wiring & Distribution Boards All Floors | 10 | 11-Jun-26 | 23-Jun-26 | 06-Jun-25 | 18-Jun-25 |
| A7740 | HVAC Ductwork, AHUs, FCUs & Outdoor Units All Zones | 10 | 11-Jun-26 | 23-Jun-26 | 06-Jun-25 | 18-Jun-25 |
| A7750 | Plumbing, Sanitary & Drainage Pipework All Floors | 15 | 11-Jun-26 | 29-Jun-26 | 06-Jun-25 | 24-Jun-25 |
| A7760 | Fire Fighting System Sprinkler, Hydrant & Alarm | 15 | 11-Jun-26 | 29-Jun-26 | 06-Jun-25 | 24-Jun-25 |
| A7770 | Lifts / Elevators Rail Alignment, Machinery & Car Fit-Out | 20 | 11-Jun-26 | 04-Jul-26 | 06-Jun-25 | 30-Jun-25 |
| A7780 | Building Management System (BMS), CCTV & Access Control | 15 | 26-Jun-26 | 13-Jul-26 | 21-Jun-25 | 08-Jul-25 |
| **LAB CEP.PHASE3.FW FINISHING WORKS** | | 57 | 11-Jun-26 | 17-Aug-26 | 06-Jun-25 | 12-Aug-25 |
| A7790 | External Facade Curtain Wall, Aluminium Cladding & Glazing | 15 | 11-Jun-26 | 29-Jun-26 | 06-Jun-25 | 24-Jun-25 |
| A7800 | Painting & Wall Finishes All Internal Areas (All Floors) | 30 | 03-Jul-26 | 07-Aug-26 | 28-Jun-25 | 02-Aug-25 |
| A7810 | False Ceiling Gypsum Board / Armstrong Grid (Mall, Office, Hot | 10 | 03-Jul-26 | 15-Jul-26 | 28-Jun-25 | 10-Jul-25 |
| A7820 | Doors, Windows, Glass Partitions & Hardware Fittings | 12 | 20-Jul-26 | 01-Aug-26 | 15-Jul-25 | 28-Jul-25 |
| A7830 | External Site Development Paving, Landscaping & Car Park M | 12 | 03-Jul-26 | 17-Jul-26 | 28-Jun-25 | 12-Jul-25 |
| A7840 | Internal Signage, Wayfinding, Branding & Tenant Signage Zon | 10 | 05-Aug-26 | 17-Aug-26 | 31-Jul-25 | 12-Aug-25 |
| **LAB CEP.PHASE3.TC TESTING & COMMISSIONING** | | 15 | 23-Jun-26 | 10-Jul-26 | 18-Jun-25 | 05-Jul-25 |
| A7850 | Electrical Systems Testing & Commissioning (HV/LV, Earthing, | 5 | 23-Jun-26 | 29-Jun-26 | 18-Jun-25 | 24-Jun-25 |
| A7860 | HVAC Systems Testing, Air Balancing & BMS Integration | 5 | 23-Jun-26 | 29-Jun-26 | 18-Jun-25 | 24-Jun-25 |
| A7870 | Plumbing & Drainage Pressure Test & Commissioning | 5 | 29-Jun-26 | 04-Jul-26 | 24-Jun-25 | 30-Jun-25 |
| A7880 | Fire Fighting System Full Load Test & Rescue 1122 Certificatio | 5 | 29-Jun-26 | 04-Jul-26 | 24-Jun-25 | 30-Jun-25 |
| A7890 | Lift / Elevator Performance Test, Load Test & PEPA Certificatior | 5 | 04-Jul-26 | 10-Jul-26 | 30-Jun-25 | 05-Jul-25 |
| **LAB CEP.PHASE3.LDAINS LDA INSPECTION** | | 79 | 29-Jun-26 | 29-Sep-26 | 24-Jun-25 | 24-Sep-25 |
| A7900 | Internal QA/QC Walkthrough & Snagging List Preparation (All F | 11 | 17-Aug-26 | 29-Aug-26 | 12-Aug-25 | 25-Aug-25 |
| A7910 | Snagging & Defect Rectification Works | 10 | 29-Aug-26 | 10-Sep-26 | 25-Aug-25 | 05-Sep-25 |
| A7920 | LDA Final Inspection Structural Compliance & Building Services | 6 | 10-Sep-26 | 17-Sep-26 | 05-Sep-25 | 12-Sep-25 |
| A7930 | WASA Final Inspection & Permanent Metered Water Connectic | 3 | 04-Jul-26 | 08-Jul-26 | 30-Jun-25 | 03-Jul-25 |
| A7940 | LESCO Final Inspection & Permanent HV Power Energization | 3 | 29-Jun-26 | 02-Jul-26 | 24-Jun-25 | 27-Jun-25 |
| A7950 | Fire Department Final Clearance & Safety Certificate | 3 | 04-Jul-26 | 08-Jul-26 | 30-Jun-25 | 03-Jul-25 |
| A7960 | LDA Completion Certificate / Occupancy Permit (Issued) | 10 | 17-Sep-26 | 29-Sep-26 | 12-Sep-25 | 24-Sep-25 |
| **LAB CEP.PHASE3.PH PROJECT HANDOVER** | | 11 | 29-Sep-26 | 12-Oct-26 | 24-Sep-25 | 07-Oct-25 |
| A7970 | As-Built / Record Drawings Preparation & Submission (All Disci | 10 | 29-Sep-26 | 10-Oct-26 | 24-Sep-25 | 06-Oct-25 |
| A7980 | O&M Manuals, Warranties & Guarantees Compilation | 11 | 29-Sep-26 | 12-Oct-26 | 24-Sep-25 | 07-Oct-25 |
| A7990 | Final Account & Project Cost Report Submission to Client | 10 | 29-Sep-26 | 10-Oct-26 | 24-Sep-25 | 06-Oct-25 |
| A8000 | Physical Key Handover to Client Ajwa Builders & Developers (F | 1 | 10-Oct-26 | 12-Oct-26 | 06-Oct-25 | 07-Oct-25 |

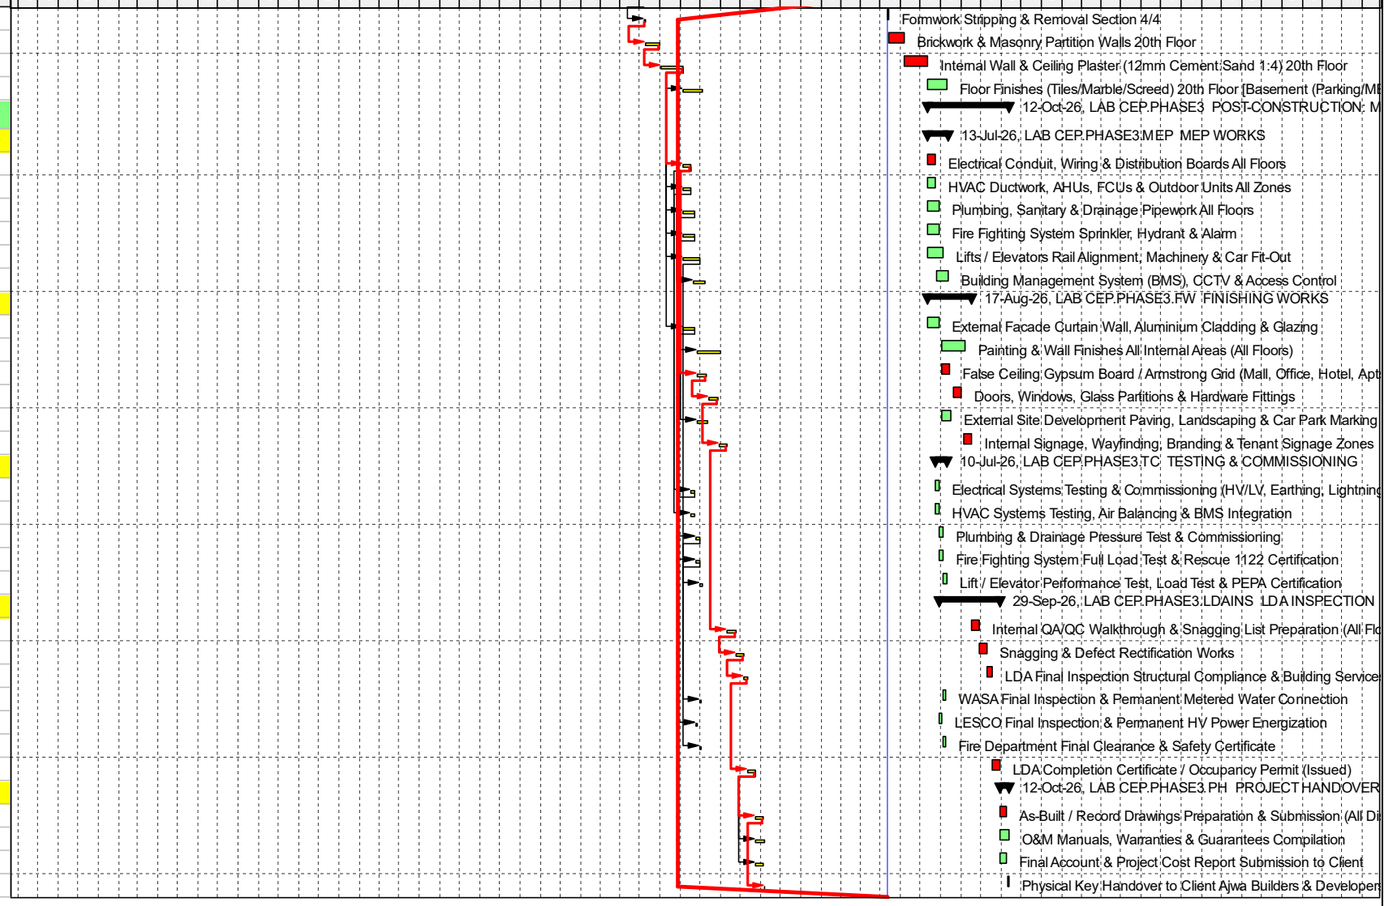


Actual Level of Effort | Actual Work | Critical Remaining Work

Primary Baseline | Remaining Work | Milestone



TASK filter: All Activities

© Oracle Corporation
